

ATWS Worksite Protection for Corrimal Condition

Monitoring equipment maintenance

DOCUMENT NO.	D2022/2794
WORK DESCRIPTION	Routine Maintenance activities - Condition monitoring equipment maintenance
WPP Number	CMO4BWS 10120
SCOPE:	<p>Routine maintenance activities performed by Condition Monitoring Operations team.</p> <ul style="list-style-type: none"> on the Up Main and Down Main Illawarra lines between 76.250 km that does not involve the use of tools or equipment, or using tools which can be easily and immediately removed from the track by one person and are light, non-powered hand tools, or light battery powered tools or devices this protected worksite is outside yard limit
AUTHORISATIONS:	<p>Protection Officer, ATWS Operator (Operator) & ATWS Installer (Installer):</p> <ul style="list-style-type: none"> Protection Officer (PO) Level 1 – 4, and WATWS – Wireless Automatic Track Warning System <p>Dedicated Lookout: (PO) Level 1 - 4, or Handsignaller 1 - 2</p>
PERSONAL PROTECTIVE EQUIPMENT	<ul style="list-style-type: none"> High visibility vest, boots, high visibility lookout sleeve
SAFETY CONTROLS – Lookout Working (ATWS) arrangements:	<p>Automatic Track Warning System (ATWS) - provides visual and audible warning for workers</p> <ul style="list-style-type: none"> ATWS sensor for Down direction running on the Up Illawarra line at 75.129 km ATWS sensor for Down direction running on the Down Illawarra line at 75.129 km ATWS sensor for Up direction running on the Up Illawarra line at 77.125 km ATWS sensor for Up direction running on the Down Illawarra line at 77.125 Km Dedicated lookout(s) at the worksite for unsignalled movements. <p>IMPORTANT!</p> <ul style="list-style-type: none"> This document must not be used to install or adjust the ATWS sensors All sensors in the plan and shown on the diagram must be connected to transmit a warning
PRESTART REQUIREMENTS:	<ul style="list-style-type: none"> Refer to D2015-45354 Wireless ATWS (Automatic Track Warning System) to install or remove sensors
FURTHER INFORMATION:	<p>Refer to “D2015-45354 Wireless ATWS (Automatic Track Warning System)” for detailed instructions to set-up, connect, test and operate the ATWS system with pre-installed ATWS sensors</p> <ul style="list-style-type: none"> NLA 410 Sutherland to Wollongong

Required ATWS Equipment		
Item	Description	Quantity
Aerial	Telescopic Aerial	3
Assembly Kit	Orange Bag with Tools	1
Battery ZA24-2.9	Small battery for Junction Box & Transmitter	8
Device Frame	Protective Frame	3
F500-AB Junction Box	Receiver Device	4
F500-SEN Train Sensor	Sensor	4
Housing for Aerial	Housing for Telescopic Aerial	3
KF5-5 Extension Cable	Extension Cable (5m) for F500-SEN to F500-AB	2
Mobile Backpack	Harness for Device	0
Pouch	Pouch for small battery	4
Tripod	Tripod for Device	3
ZFS Radio Transmitter	Radio Transmitter Device	2
ZPW Warning Unit	Control & Warning Device	1

ATWS Worksite Protection for Corrimal Condition

Monitoring equipment maintenance

Protection Officer/Operator assessment checklist

Protection Officer's name:		Yes <i>(Tick if yes)</i>
This document has not expired 12 months beyond the issue date.		
SWI details and protection arrangements have been reviewed and validated for the assessed worksite location, including: <ul style="list-style-type: none"> • On-site safety assessment has been completed for relevancy of works being undertaken • The required protection details, environment and tasks are unchanged from the details of this SWI • All boxes have been ticked if applicable and crossed if not applicable • All fields have been completed 		
Corridor Safety Number	Protection Officer Signature	Date

Warning



If an above item does not apply, the Protection Officer must not use this Safe Work Instruction. A new worksite protection plan must be completed in accordance with NRF 014 Worksite Protection Pre-work briefing and NRF 015 Worksite Protection Plan.

ATWS Worksite Protection for Corrimal Condition Monitoring equipment maintenance



Worksite Protection Pre-work Briefing

Briefing date:

Protection Officer details

Work location:

Scope of work:

Worksite protection: Refer to Worksite Protection Plan for details

Hazards (e.g. Site-specific hazards identified, including physical environment, human errors, plant and equipment)	Controls (to be implemented to eliminate or reduce the risk to the lowest practicable level)	Person responsible for Control
Crossing live lines	A qualified Protection Officer (PO) or Access Corridor Safety (ACS) must make a safety assessment to cross live lines in accordance with NGE200 and supervise workers who do not hold the PO or ACS qualification.	Qualified PO/ACS
Accessing Danger Zone to conduct plate test	Use appropriate safety measures as validated by a PO. Refer to diagram for minimum safety assessment.	Qualified PO
Electricity	ATWS antennae not to encroach safe approach distance to overhead wiring	Operator
Slips, trips, falls carrying ATWS equipment	Use correct manual handling techniques, secure safety boots, clear obstacles for work area and agree a safe path.	All
Approaching rail traffic	Lookout Working using approved ATWS as assessed in the plan & diagram. All points of entry have been validated and ATWS safety measures (sensors) have been installed. Confirm with the Operator that the ATWS has been tested and is operational. Workers immediately move to the designated safe place when warned. Provide ALL CLEAR handsignal after workers and equipment are in a safe place. After the warning has been cancelled, confirm there is no approaching rail traffic between the sensors and the worksite before allowing work to resume.	PO
Ineffective ATWS warnings / Adjoining / surrounding worksites	Test and confirm workers can see and hear the warning in the noisiest environment. Explain the emergency warnings. Workers to be within 50m of warning device. Workers to always remain within sight and hearing of warning unit. Radios not to be used near ATWS.	PO
Train warning time longer than expected (stopping points or ATWS equipment fault)	Workers to remain in a safe place until confirmed the ATWS is working correctly. Contact the Signaller or visually confirm the line is clear between the sensors and the worksite. Potential stopping points: Corrimal Station	PO
Adjacent live lines	Remain within the tracks being protected by the ATWS	PO
Unsignalled movements in Yard limits	Position lookout(s) in safe place. Confirm minimum sighting distance can be achieved. Test effective communication and be within sight and hearing of the workers.	PO / lookouts
Second train warning cancelled in error	Nominate a team member to confirm with the Operator when each rail traffic has completely passed the worksite. Tell the PO and workers about the second train warning. Cancel each warning after each train has completely passed the worksite.	Operator / nominated team member
Distraction	Obtain permission from PO to use electronic devices in the Danger Zone.	All
Obstructions to safe place	Agree on paths to reach designated safe places from the worksite.	PO
Electrical storms	Stop work immediately	All

**ATWS Worksite Protection for Corrimal Condition
Monitoring equipment maintenance**



Hazards (e.g. Site-specific hazards identified, including physical environment, human errors, plant, and equipment)	Controls (to be implemented to eliminate or reduce the risk to the lowest practicable level)	Person responsible for Control

Safe Work Instruction

**ATWS Worksite Protection for Corrimal Condition
Monitoring equipment maintenance**



Workplace Supervisor details

 Emergency assembly point: SWMS/SWI Ref #:
 First aid kit location: First aider:

Workplace Supervisor acknowledgement

The Workplace Supervisor acknowledges that all identified WHS and rail safety hazards have the appropriate controls in place to manage and/or eliminate the hazards.

Yes

Participant Acknowledgement

NOTE: Recipients of the briefing are to question the Briefer if they don't understand any part of this briefing.

All workers listed below acknowledge that they:

1. have been inducted to the site	6. have been briefed on the contents of the Worksite Protection Plan
2. are free from alcohol and drugs	7. have been shown the Worksite Protection Plan diagram
3. are free from the effects of fatigue	8. understand the kinds and limits of worksite protection in place
4. hold the applicable and current Rail Safety Worker Authorisation, trade licence and/or induction record e.g. Construction Industry Induction	9. have been briefed about any new hazards and controls identified during the final site inspection <i>(final site inspection must be conducted immediately before commencing work)</i>
5. must wear the appropriate Personal Protective Equipment (PPE)	

Mark each check box below with a tick if the item applies or a cross if the item does not apply.

<input type="checkbox"/> have been informed of the requirements of the electrical permit (if required)	<input type="checkbox"/> have been made aware of any hazardous materials/substances on site
<input type="checkbox"/> have been briefed on the SWMS/SWIs/documentated safe work practice for the job	<input type="checkbox"/> have been briefed on Safety Data Sheets (SDS)
<input type="checkbox"/> have been instructed in the controls recorded in this document and SWMS/SWIs	<input type="checkbox"/> have been briefed on the WHS Management plan
	<input type="checkbox"/> have been briefed on the hazards of adjoining worksites/processes.

Name	Signature	Time of briefing: hh:mm	Amendment briefing: hh:mm and initial

Worksite Protection Plan – Lookout Working

Signaller details

Protection Officer details

Planned duration

Workplace Supervisor details:

Type of work:

Worksite location

On the

between and

On the

between and

Worksite Assessment

Has the Lookout Working Prohibited Locations Register been consulted? Yes

Warning method

Minimum Warning Time Calculations

Maximum track speed

Number of ATWS Sensors used Position of ATWS Sensors and

Number of dedicated Lookouts used Position of Lookouts To

Note - Lookouts are relocated to positions within these KMs as workers move along the worksite.

<input type="text" value="7 sec"/>	+	<input type="text" value="3 sec"/>	+	<input type="text" value="10 sec"/>	=	Minimum Warning Time (MWT)	<input type="text" value="20 sec"/>	<input type="text" value="100 km/h"/>	<input type="text" value="556 metres"/>	<input type="text" value="Up Illawarra line"/>
<input type="text" value="7 sec"/>	+	<input type="text" value="3 sec"/>	+	<input type="text" value="10 sec"/>		$(S+M+10 \text{ sec} = \text{MWT})$	<input type="text" value="20 sec"/>	<input type="text" value="100 km/h"/>	<input type="text" value="556 metres"/>	<input type="text" value="Down Illawarra line"/>
<i>See Time (S)</i>		<i>Move Time (M)</i>		<i>Safe Time</i>			<i>Track speed</i>		<i>Minimum Sighting Distance as calculated</i>	

Dedicated Lookout

<input type="text" value="2 sec"/>	+	<input type="text" value="3 sec"/>	+	<input type="text" value="10 sec"/>	=	Minimum Warning Time (MWT)	<input type="text" value="15 sec"/>	<input type="text" value="25 km/h"/>	<input type="text" value="105 metres"/>
<i>See Time (S)</i>		<i>Move Time (M)</i>		<i>Safe Time</i>		$(S+M+10 \text{ sec} = \text{MWT})$	<i>Track speed</i>		<i>Minimum Sighting Distance as calculated</i>

Where are the safe places identified for the ATWS Operator, Lookouts, and workers?

Lookouts:

Workers:

Confirm mandatory first train tests were completed for all sensors Yes


Ensure the workers have been briefed about these work details Yes

NOTE: Diagrams and instructions that follow form part of this worksite protection plan.

ATWS Worksite Protection for Corrimal Condition Monitoring equipment maintenance

Tick if used

Worksite on the Up & Down Illawarra lines

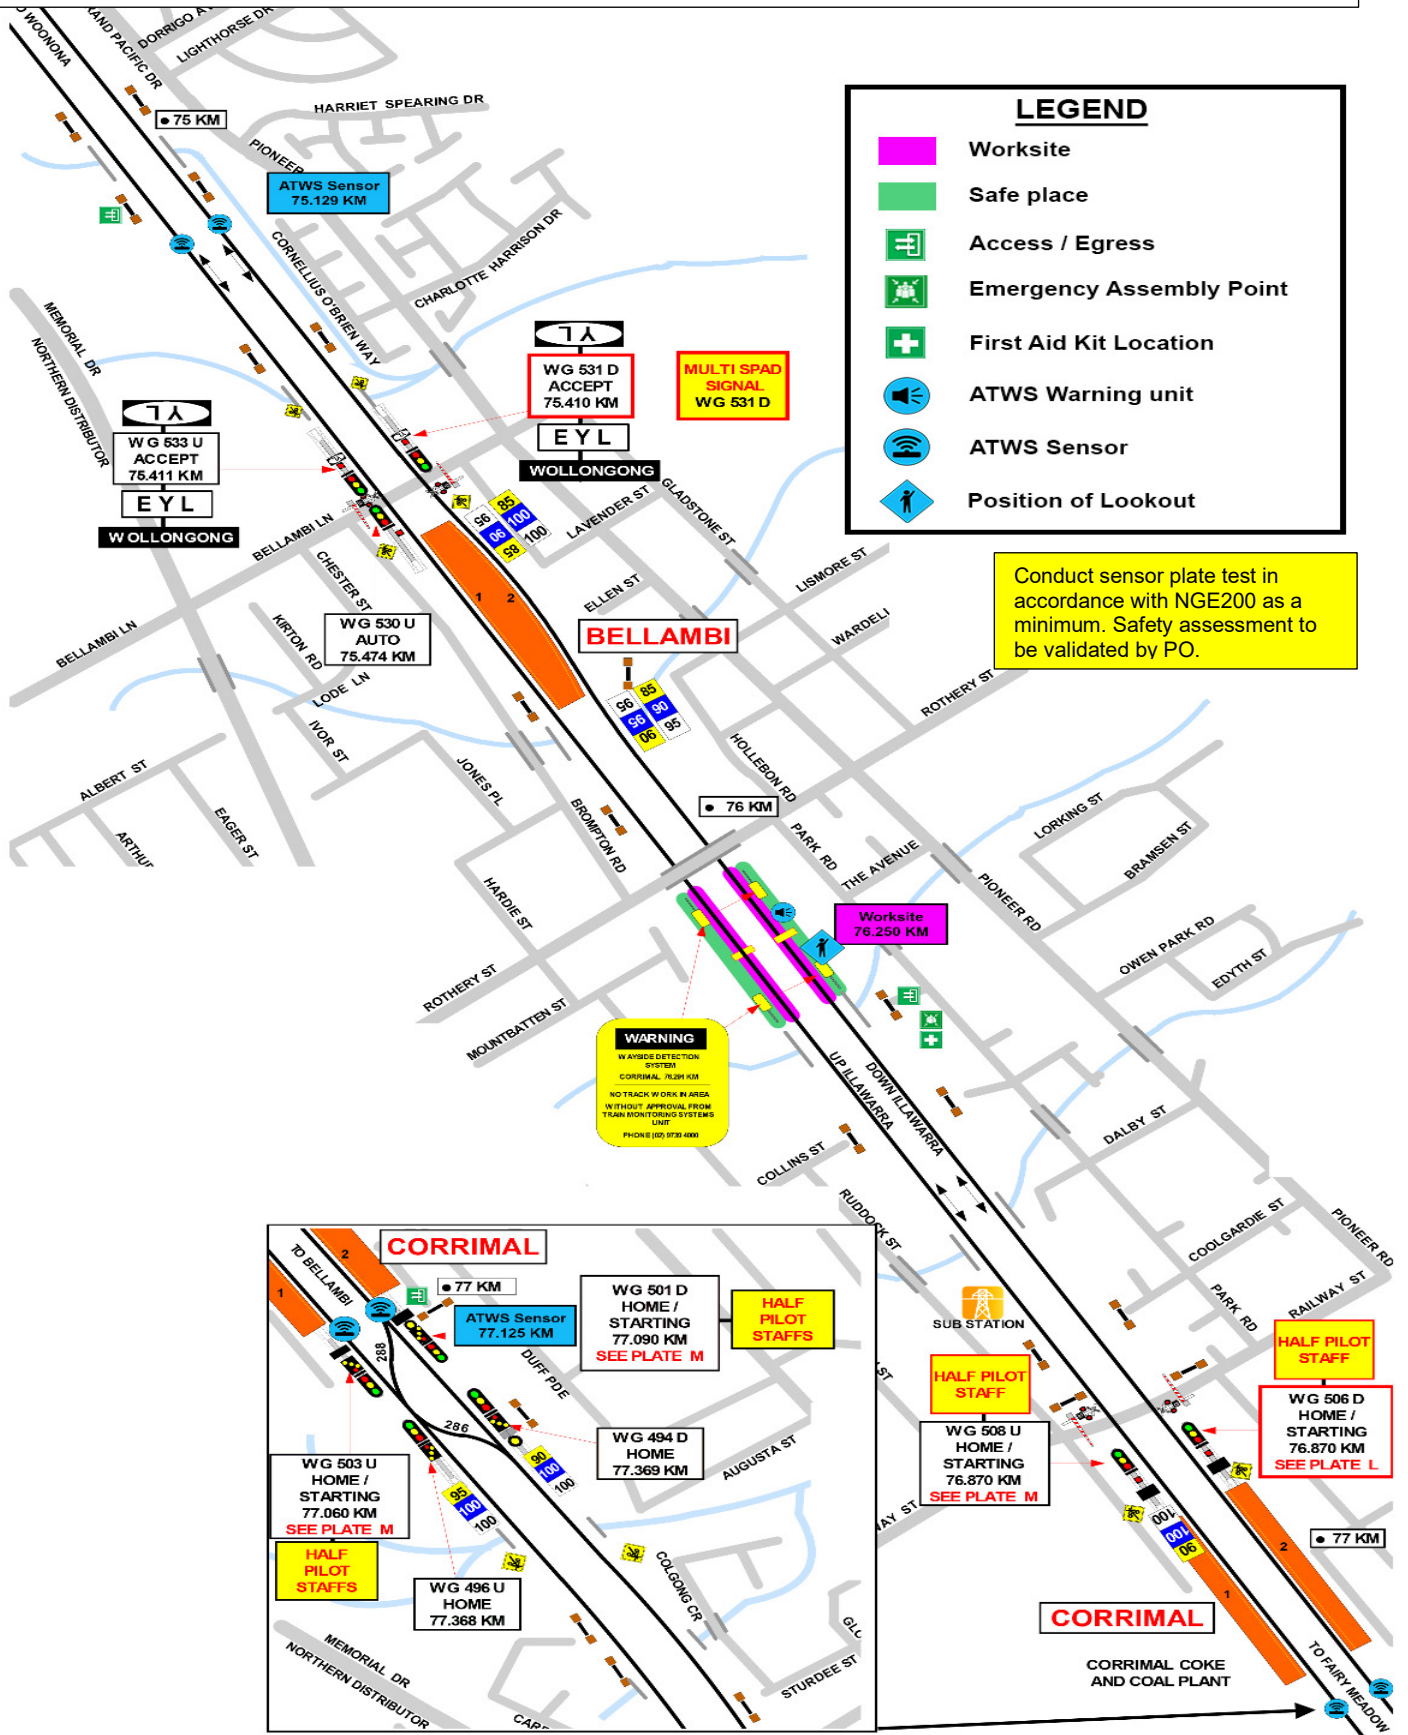

**ATWS Worksite Protection for Corrimal Condition
Monitoring equipment maintenance**



INSTRUCTIONS:	<ol style="list-style-type: none"> 1. Workers enter the rail corridor via access gate 100 76.237 D. 2. Use assets to validate worksite location on Up Main and Down Illawarra lines between 76.250 km 3. Conduct WP Pre-work briefing to set-up ATWS. 4. Tell Signaller at Wollongong North Panel about the use of lookout working with ATWS.
Tick if used <input type="checkbox"/>	<ol style="list-style-type: none"> 1. Access Up Cess 77.125 km, verify sensor label & connect to sensor cable, calibrate with test plate, connect, and turn on the transmitter.
Tick if used <input type="checkbox"/>	<ol style="list-style-type: none"> 2. Access Up Cess 75.129 km, verify sensor label, connect to sensor cable, calibrate with test plate, connect & turn on transmitter.
	<ol style="list-style-type: none"> 3. Place warning system on same side of tracks if working on one track only within sight & hearing of workers, conduct siren & light self-test, & connect to transmitter(s). 4. Record first rail traffic movement test for each sensor on ATWS Check-sheet. 5. Conduct WP Pre-work briefing for lookout working with ATWS and confirm workers have seen and heard the warning. 6. Start work when advised by the PO and move to the designated safe place when warned. 7. When work is complete, and workers and equipment are in a safe place, turn off and pack up warning unit
Tick if used <input type="checkbox"/>	<ol style="list-style-type: none"> 8. Access Up Cess to turn off and pack up transmitter unit(s).
Tick if used <input type="checkbox"/>	<ol style="list-style-type: none"> 9. Access Up Cess to turn off and pack up transmitter unit(s).
	<ol style="list-style-type: none"> 10. Access Down Cess for all workers to leave the rail corridor via access gate 100 76.237 D 11. Tell Signaller at Wollongong North Panel when work is completed, and the workers and their equipment are clear of the Danger Zone.

ATWS Worksite Protection for Corrimal Condition Monitoring equipment maintenance

Tick if used **Position of ATWS transmitter and sensor on the Down Illawarra line at 75.129 KM**



Image 1: Transmitter and sensor installation location



Image 2: Sensor access using access gate 100 75.400 U

Tick if used **Position of ATWS transmitter and sensor on Up Illawarra line at 77.125 KM**



Image 1: Transmitter and sensor installation location



Image 4: Sensor access using access gate at Corrimal Station

ATWS Worksite Protection for Corrimal Condition Monitoring equipment maintenance

(This page is optional and may be separated and given to the assigned operator to assist set-up of ATWS equipment. Refer also to Refer to "D2015-45354 Wireless ATWS (Automatic Trak Warning System)" for detailed instructions.)

Setup Stage 2: checklist for ATWS worksite warning unit		
Step	Task Description	Operator Check
1	Confirm equipment is within inspection date	
2	Confirm Audible level	
3	Confirm and set Radio Channel for Warning unit	
4	Book in ATWS sensor 1	
5	Book in ATWS sensor 2	
6	Book in ATWS sensor 3	
7	Book in ATWS sensor 4	
8	Perform Worksite Warning Test with all ATWS sensor	
9	Ensure the workers have seen the visual warning and heard the audible warning	
10	Select and Confirm Channel for the Radio Transmitter	
11	Confirm worksite warning unit is operational with Installers and advise them to lock devices & remove key	

Setup Stage 1: Checklist for ATWS transmitter and sensor		
Step	Task Description	Installer Check
1	Verify Track Label for location of sensor as per the Protection Diagram and Photos in this document	
2	Confirm equipment is within inspection date	
3	Sensor direction is per Worksite Protection Diagram and photos in this document	
4	Connect sensor cable to junction box	
5	Confirm all batteries are fully charged	
6	Connect junction box to ZFS using channel T1-T4	
7	Commence calibration and automatic self- test	
8	Perform function test using test plate	
9	Confirm transmitter booked in to correct T- channel (T1-T4)	
10	Select & confirm channel for the radio transmitter (AU3 OR AU4)	
11	Perform worksite warning test using test plate	
12	Lock device & remove key	
