

weekly notice



Monday, 07 July 2025

Sunday, 13 July 2025







See online for all Safeworking Information

www.railsafe.org.au

Safeworking information, including Weekly Notices and SAFE Notices, is available on the RailSafe website.

By accessing Weekly Notices and SAFE Notices online, you will receive safety information more quickly. Weekly Notices remain on the RailSafe website for two years; Permanent and Temporary SAFE Notices remain online as long as they are current.

Anyone needing back issues of Weekly Notices and SAFE Notices should contact the Network Rules unit.

If you are outside Sydney Trains, you can reach the RailSafe website via the following address:

www.railsafe.org.au

Other Safeworking documents, such as Network Rules, Network Procedures, Network Local Appendices, Safeworking Policies, SafeTracks flyers, and contractor information are also available online.

Director Network Standards, Systems and Quality

Sydney Trains



PUBLICATION DEADLINES AND SUBMISSION OF ARTICLES	4
REGIONAL INFRASTRUCTURE UPGRADES – NEW INTERCITY FLEET PROJECT - BLUE MOUNTAIN LINE STAGE 9A-2 COMMISSIONING OF MARKER CHANGES FOR THE AREA LITHGOW TO BLACKTOWN SII NOTICE	
REGIONAL INFRASTRUCTURE UPGRADES – NEW INTERCITY FLEET PROJECT - BML STAGE 9A2 COMMISSIONING OF POINTS CLEARED CAR SIGN AT VALLEY HEIGHTS STATION. CAR MARKER CHANGES A VALLEY HEIGHTS, GLENBROOK AND BLAXLAND STATIONS - SINCE NOTICE (DIAGRAM)	-
REGIONAL INFRASTRUCTURE UPGRADES – NEW INTERCITY FLEET PROJECT - BML STAGE 9A2 – PENRITH STATION PLATFORM 2 – TEMPORARY MARIYUNG TRAIN GUARDS USE ONLY PLATFORM EXTENSION, REMOVAL OF "10 CAR POINTS CLEARED" SIGN & CAR MARKER CHANGES SINCE NOTICE	14
RICHMOND (WEST) – CONVERSION OF FRAME D TO POWER OPERATION AND PROVISION OF SIGNALLED ROUTES AND INTERMEDIATE TRAINSTOPS FOR THE UP STORAGE ROAD	17
STATUS OF TOM NOTICES	18
STATUS OF PERMANENT SAFE NOTICES	20
STATUS OF NETWORK MANUALS AND FORMS	21
DISTRIBUTION OFFICERS	23



PUBLICATION DEADLINES AND SUBMISSION OF ARTICLES

Dates of the next four Weekly Notices and deadlines for articles are:

Weekly Notice	For Week	Deadline
29	14/07/2025 – 20/07/2025	10/06/2025
30	21/07/2025 – 27/07/2025	17/06/2025
31	28/07/2025 - 03/08/2025	24/06/2025

To meet printing and distributing schedules, articles for a Weekly Notice must be received by its deadline.

Articles submitted after a deadline will be published in the next issue of the Weekly Notice. This may result in information not being distributed in time for it to be acted upon.

When submitting articles, please include your name, position title, telephone numbers and email address at the end of the articles as shown below:

Steve Swanson

Network Rules SpecialistTel:0428416505Email:stephen.swanson@transport.nsw.gov.au

Rail<mark>Safe</mark>

REGIONAL INFRASTRUCTURE UPGRADES – NEW INTERCITY FLEET PROJECT - BLUE MOUNTAIN LINE STAGE 9A-2 COMMISSIONING OF CAR MARKER CHANGES FOR THE AREA LITHGOW TO BLACKTOWN. - SINCE NOTICE

Since 18:00 hours on **Sunday**, **1 June 2025**, the following works were carried out carried out:

• New post mounted car markers signs listed in table 2 were installed with white crosses.

The following works were commenced on **Wednesday**, **18 June 2025**, and were completed on **Friday**, **20 June 2025**.

- Commissioning of new platform car marker & trackside stopping sign arrangements at the following stations & respective platforms to accommodate the new 4,6,8 and 10 car NIF trains.
- Affected stations comprise: Zig Zag (1,2), Katoomba (1,2), Wentworth Falls (1,2), Bullaburra (1), Lawson (1,2), Woodford (1,2), Linden (1,2), Faulconbridge (1,2), Springwood (1,2), Warrimoo (1,2) and Blacktown (4,5,6,7)
- Removal of diagonal white tape from car markers installed in an earlier stage. Details listed in table 1.
- Additional car marker changes as listed in table 02 below.
- No change to the existing Lithgow Station '10' carmarker on platform 1 country end fence. It will remain in situ and not removed as previously advertised in the initial Weekly Notice.

Table 01 – Diagonal white tape Removal from early installation of new platform & Post Mount car marker sign details. All to be commissioned into use.



Station	Platform	New CM Sign	Installation Position (from the respective platform fenceline)
Wentworth	1 Sydney	10	approx. 25m to city from
Falls	End		the fence
Wentworth	2 Country	10	approx. 17m to country
Falls	End		from the fence
Bullaburra	1 Sydney	10	approx. 25m to city from
	End		the fence
Lawson	1 Sydney	10	approx. 18m to city from
	End		the fence
Lawson	2 Country	10	approx. 19m to country
	End		from the fence
Woodford	1 Sydney	10	approx. 25m to city from
	End		the fence
Woodford	2 Country	10	approx. 18m to country
	End		from the fence.
Linden	1 Sydney	8	approx. 38m to city from
	End		the fence
Linden	1 Sydney	10	approx. 78m to city from
	End		the fence
Linden	2 Country	8	approx. 40m to city from
	End		the fence
Linden	2 Country	10	approx. 100m to city from
	End	-	the fence
Faulconbridge	1 Sydney	10	approx. 16.0m to city
	End	-	from the fence
Faulconbridge	2 Country	10	Installed on OHWS
, and a second sec	End		approx. 17m to country
			from the fence
Springwood	1 Sydney	10	approx. 16m to city from
opgeea	End		the fence
Springwood	1 Country	10	approx. 16m to country
Springwood	End	10	from the fence
Springwood	2 Sydney	10	approx. 18m to city from
Springwood	End		the fence
Springwood	2 Country	10	approx. 18m to country
Springwood	End		from the fence
Warrimoo	1 Sydney	8/6/4	approx. 8m to country
vvariini00	End	0/0/4	from the fence
Warrimoo	1 Sydney	10	
variiii00	End		approx. 30m to city from the fence
	ENU		



Warrimoo	2 Country	10	approx. 37m to country
	End		from the fence

Table 02 – Additional Car Marker Changes.

Station	Platform	Carmarker Sign changes
Lithgow	1 Country End	Existing '10' carmarker on fence will remain in situ and will not be removed as previously indicated.
Zig Zag	1 Sydney End	 Existing combined '10/8/6/4' carmarker sign on fence removed & replaced with New post mounted "4" carmarker installed approx. 72.5m to city from the fence. New post mounted "6" carmarker installed approx. 113.2m to city from the fence. New post mounted "8" carmarker installed approx. 154m to city from the fence. New post mounted "10" carmarker installed
		approx. 194.7m to city from the fence.
Zig Zag	2 Country End	Existing combined '10/8/6/4' carmarker on the fence will be removed & replaced withi. New post mounted "4" carmarker installed approx. 72.5m to country from the fence.
		 ii. New post mounted "6" carmarker installed approx. 113.2m to country from the fence. iii. New post mounted "8" carmarker installed approx. 154m to country from the fence. iv. New post mounted "10" carmarker installed approx. 194.7m to country from the fence.

Station	Platform	Carmarker Sign changes
Katoomba	1 Sydney End	Existing '10' carmarker sign on the fence and '10' and '8' carmarker on the coping will be removed and replaced with New '10/8' carmarker sign on the fence.



Katoomba	1 Country End	 Existing '10' carmarker sign on the fence and the existing '10' and '8' carmarker on the coping will be removed and replaced with New "8" carmarker painted on coping. Adjacent to the existing "10" Carmarker. New '10/8' carmarker sign on the fence.
Katoomba	2 Country End	Existing '10' carmarker sign on the fence and the existing '10' and '8' carmarker on the coping will be removed and replaced with new '10/8' carmarker sign on the fence.
Wentworth Falls	1 Sydney End	Existing '10' carmarker sign on the fence removed
Wentworth Falls	2 Country End	Existing "10/8/6" carmarker sign on the fence will be removed and replaced with new '8/6' carmarker sign on the fence.
Bullaburra	1 Sydney End	Existing combined "10/8/6" carmarker sign on the fence will be removed and replaced with new '8/6' carmarker sign on the fence.
Lawson	1 Sydney End	Existing "10" carmarker on the coping removed
Lawson	2 Country End	Existing "10" carmarker on the fence removed
Linden	1 Sydney End	Existing combined "10/8/6/4" carmarker sign on the fence will be removed and replaced with a New '6/4' carmarker sign on the fence.
Linden	2 Country End	Existing combined "10/8/6/4" carmarker sign on the post and existing '10/8/6/4" carmarker on the coping will be removed and replaced with i. New '6/4' carmarker sign on the existing post. ii. New '6/4' carmarker painted on coping.
Falconbridge	1 Sydney End	Existing '10' carmarker sign on the fence removed
Falconbridge	2 Country End	Existing combined '10/8' carmarker sign on the fence and '10/8' carmarker on the coping will be removed and replaced with new "8" carmarker painted on coping.
Springwood	1 Sydney End	Existing combined "10/8/6/4" carmarker sign on the fence will be removed and replaced with a i. new '8/6' carmarker sign on the fence ii. new "4" carmarker painted on coping approx.10.5m from the fence.



Springwood	1 Country End	Existing combined "10/8/6" carmarker sign on the fence will be removed and replaced with New '8/6' carmarker sign on the fence.		
Springwood	2 Sydney End	Existing combined "10/8" carmarker sign on the fence will be removed and replaced with New '8' carmarker sign on the fence.		
Springwood	2 Country End	Existing combined "10/8/6" carmarker sign on the fence will be removed and replaced with New '8/6' carmarker sign on the fence.		
Warrimoo	1 Sydney End	Existing combined '10/8/6' carmarker on the fence and '4' carmarker on the coping will be removed and replaced with New '8/6/4' carmarker painted on coping.		
Warrimoo	2 Country End	Existing "10/8" carmarker sign on the fence will be removed and replaced with New '8' carmarker sign on the fence.		
Lapstone	1 Sydney End	 Existing "10/8" carmarker sign on the fence will be removed and replaced with i. New "8" carmarker sign on the fence ii. new post mounted "10" Carmarker installed approx.29.5m to city from the fence. 		
Lapstone	2 Country End	 Existing "10/8" carmarker sign on the fence & the coping will be removed and replaced with new "8" carmarker sign on the fence and the coping new post mounted "8" carmarker installed approx. 29.5m to country from the fence. 		
Blacktown	4 Country End	Existing '10' carmarker sign on the fence will be removed and replaced with new post mounted "10" carmarker installed approx. 3.7m to country from the fence.		
Blacktown	5 Sydney End	Existing '10' carmarker sign on the fence will be removed and replaced with new post mounted "10" carmarker installed approx. 5.3m to city from the fence.		
Blacktown	5 Country End	Existing '10' carmarker sign on the fence will be removed and replaced with new post mounted "10" carmarker installed approx. 3.8m to country from the fence.		
Blacktown	6 Sydney End	Existing '10' carmarker sign on the fence will be removed		



Blacktown	6 Country End	Existing '10' carmarker sign on the fence and existing '10' carmarker on the coping will be removed and
		replaced with new post mounted "10" carmarker installed approx. 5.3m to country from the fence.
Blacktown	7 Sydney End	Existing '10' carmarker sign on the fence will be removed
Blacktown	7 Country End	Existing '10' carmarker sign on the fence and '10' carmarker on the coping will be removed and replaced with New "10" carmarker fix onto bridge abutment approx. 5.3m to country from the fence.

VER 18062025

Gordon Lo

Design Manager, T4T Mob: +61 2 8284 2231 E-mail: Glo@transfort.com.au

Shannon Jarvis

Construction Manager, T4T Mob: 0408 450 523 Email: sjarvis@TransforT.com.au

Rail<mark>Safe</mark>

REGIONAL INFRASTRUCTURE UPGRADES – NEW INTERCITY FLEET PROJECT - BML STAGE 9A2 COMMISSIONING OF POINTS CLEARED 10 CAR SIGN AT VALLEY HEIGHTS STATION. CAR MARKER CHANGES AT VALLEY HEIGHTS, GLENBROOK AND BLAXLAND STATIONS - SINCE NOTICE

Since 02:00 hours on **Monday, 2 June 2025**, the following works were carried out at Valley Heights Station:

- Installation of a post mounted "POINTS CLEARED 10 CARS" sign with a white cross on the DOWN MAIN (within VALLEY HEIGHTS, PLATFORM 2 limits) at approx. 77.331km.
- Installation of a new post mounted "10" Carmarker with a white cross approx. 30.45m to city from the platform 1 Sydney End fence.

The following works were completed on Wednesday, 18 June 2025.

 Removal of the white Cross and Commissioning of the new "POINTS CLEARED 10 CARS" post mounted sign on the DOWN MAIN (within VALLEY HEIGHTS, PLATFORM 2 limits) at approx. 77.331km as indicated in the Driver's Diagram in this Since Notice.

The following works were completed on **Friday**, **20 June 2025**.

- Car marker changes as listed in table 02 below.
- Commissioning of the new platform car marker & trackside stopping sign arrangements at the Valley Heights, Glenbrook and Blaxland stations to accommodate the new 4,6,8 and 10 car NIF trains as listed in Tables 1 & 2 below.

Table 01 – Diagonal white tape removal from early installation of new post mount car marker sign details.

Station	Platform	New post mounted Carmarker S	Installation Position (from the respective platform
Valley Heights	1 Sydney End	10	approx. 43m to city from the fence



Valley	2 Sydney	10	approx. 43m to city from the fence
Heights	End		
Valley	2 Country	10	approx. 39m to country from the fence
Heights	End		
Blaxland	1 Sydney	8	approx. 5m to city from the fence
	End		
Blaxland	1 Sydney	10	approx. 45m to city from the fence
	End		

Table 02 – Car Marker changes.

Station	Platform	Carmarker changes (from the respective platform fenceline)
Valley Heights	1 Sydney End	 Existing combined "10/8" carmarker sign on the fence and existing post mounted '10/8' carmarker will be removed and replaced with New '8' carmarker painted on coping at the fenceline. New post mounted "10" carmarker installed approx. 30.45m to city from the fence.
Valley Heights	2 Sydney End	Existing combined "10/8" carmarker sign on the fence will be removed and replaced with New '8' carmarker painted on coping.
Valley Heights	2 Sydney End	Existing combined "10/8/6" carmarker sign on the fence will be removed and replaced with New '8/6' carmarker sign on the fence.
Blaxland	1 Sydney End	Existing combined "10/8" car marker sign on fence will be removed and replaced with a new "8H" sign on the fence
Glenbrook	1 Sydney End	"4" carmarker on coping relocated approx. 73m from the fence.

VER 18062025 DIAGRAM VER 16042025



Matthew Ward

Signalling Commissioning Engineer, JMDR Mob: 0418 607 593 Email: matthew.ward@jmdr.com

Anthony Matthews


Senior Project Engineer -ETCS, Sigtech Solutions Mob: 0409 313 148 Email: anthony.matthews@sigtechsolutions.com.au

Gordon Lo

Design Manager, T4T (Car marker Changes) Mob: +61 2 8284 2231 E-mail: Glo@transfort.com.au

Shannon Jarvis

Construction Manager, T4T Mob: 0408 450 523 Email: sjarvis@TransforT.com.au

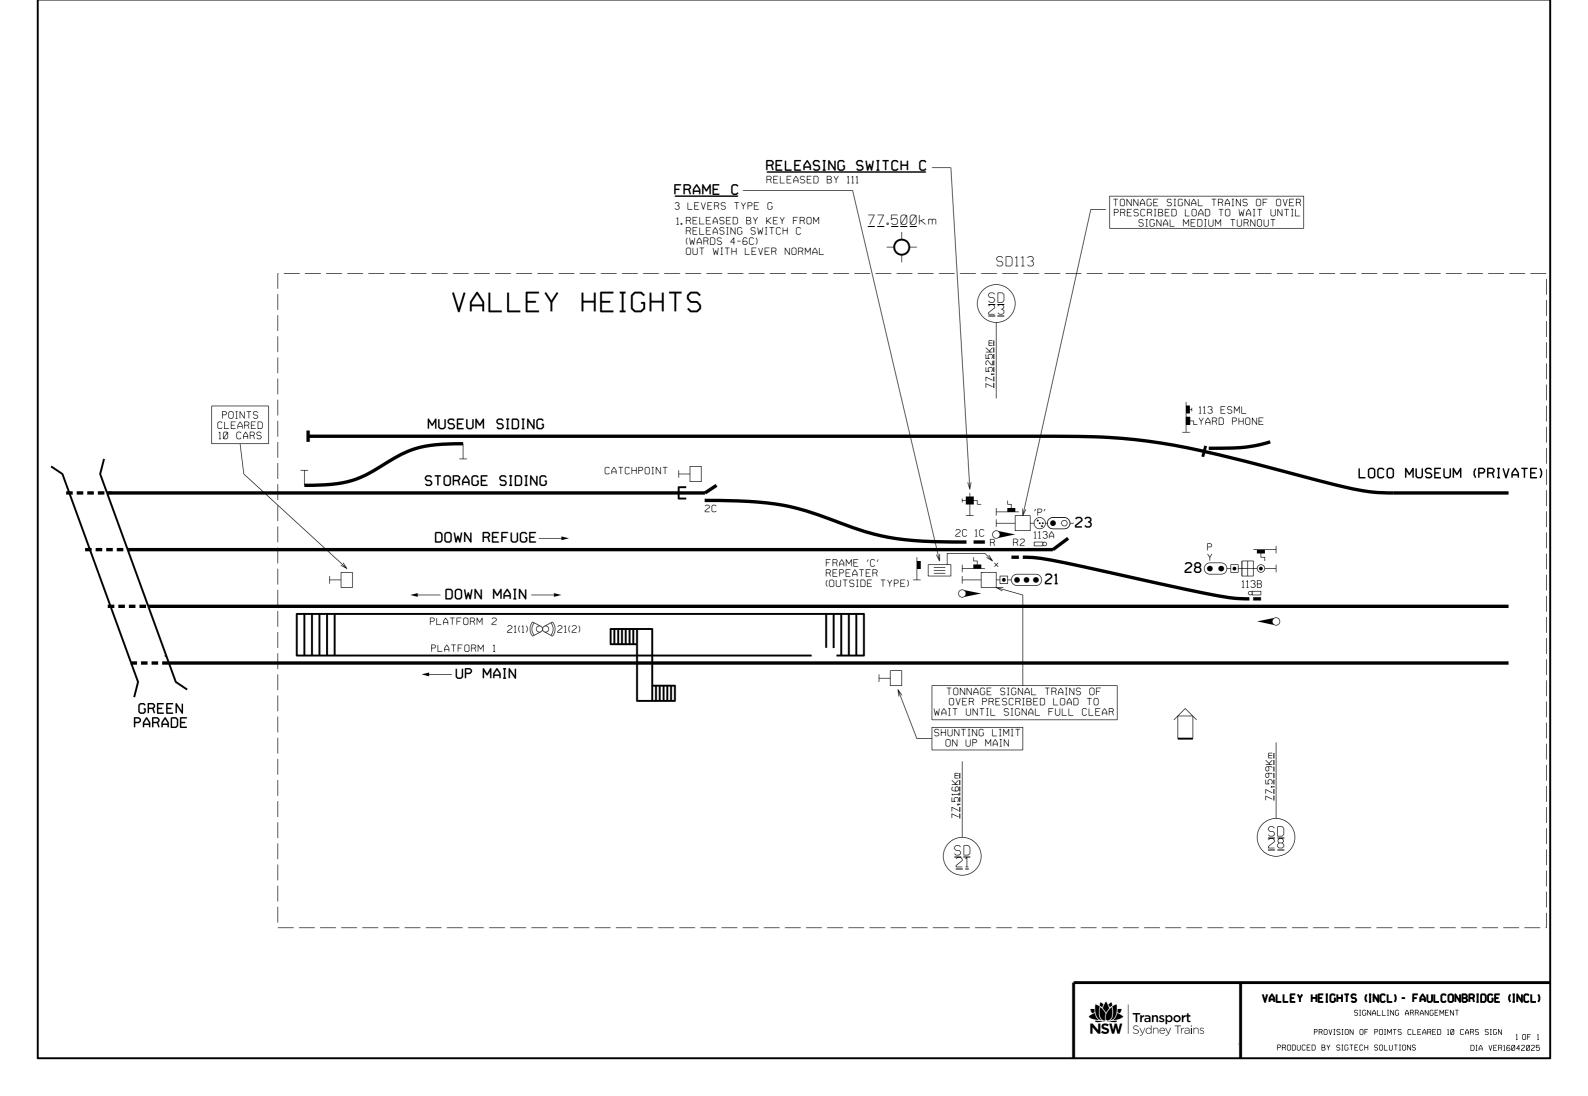

Rail<mark>Safe</mark>

REGIONAL INFRASTRUCTURE UPGRADES – NEW INTERCITY FLEET PROJECT - BML STAGE 9A2 – PENRITH STATION PLATFORM 2 – TEMPORARY MARIYUNG TRAIN GUARDS USE ONLY PLATFORM EXTENSION, REMOVAL OF "10 CAR POINTS CLEARED" SIGN & CAR MARKER CHANGES. -SINCE NOTICE

Since **Monday, 2 June 2025**, the following works were carried out:

- Construction of a temporary Mariyung Train Guards use only platform extension at the city end of platform 2 at Penrith. Refer to diagram 1 below for details.
- This will be in use until a permanent platform extension is completed in a later stage.
- Installation of a "10" Carmarker sign with a white cross on the new fenceline for the extended temporary platform.

The following works were completed on Wednesday, 18 June 2025.

• Removal of the existing Penrith Platform 2 City End "Points Cleared 10 Cars" sign.

The following works were completed on Friday, 20 June 2025.

• Commissioning of the new platform car marker & trackside stopping sign arrangements at Penrith to accommodate the new 4,6,8 and 10 car NIF trains. Listed in table 1 below.

Station	Platform	Carmarker changes	
Penrith	1 Sydney	Existing "8" carmarker sign on the fence and '8'	
	End	carmarker on the coping will be removed and replaced	
		with new '8' carmarker on coping approx. 2.1m from	
		the fence.	
Penrith	1 Country	Existing '8' carmarker on the coping will be removed	
	End	and replaced with New '8' carmarker on coping at	
		approx. 2.8m from the fence.	
Penrith	2 Country	New '10' carmarker sign on the new fenceline position	
	End	for the extended temporary platform.	

Table 1: Penrith Car Marker Changes



PLATFORM EXTENSION PLATFORM EXTENSION PLATFORM 2 PLATFORM 1 TRAK - UP MAN PLATFORM 1 TRAK - Not PLATFORM noo TRAK - Not PLATFORM noo

Diagram 1: Penrith Car Marker Changes

VER 18062025

Matthew Ward

Signalling Commissioning Engineer, JMDR Mob: 0418 607 593 Email: matthew.ward@jmdr.com

Anthony Matthews

Senior Project Engineer -ETCS, Sigtech Solutions Mob: 0409 313 148 Email: anthony.matthews@sigtechsolutions.com.au

Gordon Lo

Design Manager, T4T (Car Marker Changes) Mob: +61 2 8284 2231 E-mail: Glo@transfort.com.au



Shannon Jarvis

Construction Manager, T4T Mob: 0408 450 523 Email: sjarvis@TransforT.com.au



RICHMOND (WEST) – CONVERSION OF FRAME D TO POWER OPERATION AND PROVISION OF SIGNALLED ROUTES AND INTERMEDIATE TRAINSTOPS FOR THE UP STORAGE ROAD

The work to convert Frame D to power operation, provide signalled routes and intermediate trainstops for the Up Storage Road at Richmond, **previously advertised in Weekly Notices 23 & 24 – 2025 did not take place and will be re-advertised at a later date.**

VER 20062025

Rhoel Del Rosario

Commissioning Engineer Signalling Sydney Trains Mobile: 0413450361 Email: RHOEL.DELROSARIO@transport.nsw.gov.au

Sudipta Dey

Signal Design Engineer Signalling & Control Systems, Engineering & System Integrity Email: sudipta.dey@transport.nsw.gov.au



STATUS OF TOM NOTICES

Number	Title	Issued	Effective
018 – 2007	Emergency equipment boxes Rail	01/11/07	19/11/07
010 – 2012	48 Class: Train Operations Manual (TOM)	25/10/12	04/11/12
003 – 2013	48 Class: Wheels	07/02/13	10/02/13
015 – 2013	OMET 200: Minimum Standards for Electric Trains	30/05/13	09/06/13
002 – 2014	OMET 220: Wheelslip light indications	20/02/14	02/03/14
004 – 2016	OMET 262: Failure of Train Management System	14/07/16	24/07/16
004 – 2017	TWP 174 Ice Radio	20/07/17	31/07/17
018 - 2017	Amendment to OMET 200	14/12/17	24/12/17
012 – 2018	OMET 228 Control Circuit Failure	23/08/18	02/09/18
005 – 2018	OMET 242 Reverser handle jams in forward or reverse	18/08/18	28/08/18
006 – 2018	OMET 250 Applying power from the rear	18/08/18	28/08/18
008 – 2018	TWP 154 Responding to incapacitated Driver/Guard	18/08/18	28/08/18
016 - 2018	Network Rules Operational standards update	17/08/18	27/08/18
003 - 2019	OMET 264: Minimum Tractive Effort Requirements	21/02/19	03/03/19
012 – 2019	TWP 192: Working Trains Out of service	21/02/19	03/03/19
007 – 2019	TWP 136 Defective wheels	06/03/19	24/03/19
008 – 2019	TWP 190 Automatic Train Protection	06/03/19	24/03/19
009 – 2019	Train crew relieved in service & relay driver	06/03/19	24/03/19
004 – 2019	TWP 118 Reporting Faults	11/04/19	28/04/19
004 - 2020	TWP 124 Defective Brakes	20/05/20	08/06/20
005 - 2020	TWP 126 Defective Automatic Brakes	20/05/20	08/06/20
012 - 2020	WAR 202 Bogie Faults	20/05/20	08/06/20
011 - 2020	TWP 162 Train Crew Bell Signals	02/06/20	15/06/20
014 - 2020	TWP 112 Changing ends	20/07/20	03/08/20
017 - 2020	Operating Tangara, OSCAR, Millenium and Waratah with	07/12/20	14/12/20
	deflated air springs in the city underground		
011 - 2021	Exception to OMET 200 & 350	17/11/21	29/11/21
005 - 2022	TWP 160 Driver procedure at stations	21/04/22	08/05/22
023 - 2022	Exception to OMET 254 Topside Preparation Locations	16/08/22	22/08/22
028 - 2022	Testing of Tangara Sets fitted with European Train Control System (ETCS) Level 1 & Level 2 (In cab	08/12/22	16/12/22
	signalling) equipment at Mortdale Maintenance Centre		
027 - 2022	TWP 150: Damaged or Missing Window Glass	27/09/22	10/10/22
014 - 2023	Use of Automatic Train Protection (ATP) equipment on	20/02/23	05/03/23
017 0000	Millennium trains	07/02/02	20 (02 (22
017 - 2023	TWP 138 Assisting Trains using Emergency Couplers	07/03/23	20/03/23
022 – 2023	WB Radios on Waratah, Oscar, Millenium, Tangara and K sets	05/04/23	23/04/23
023 - 2023	OSCAR trains fitted with Automatic Train Protection (ATP) equipment	19/06/23	26/06/23
028 – 2023	TWP 176: Wayside Train Condition Monitoring	07/08/23	21/08/23
029 - 2023	Testing of an OSCAR Set (H5) with ETCS Level 2	01/09/23	04/09/23
	equipment	· ·, · ·, - ·	.,,
026 – 2023	TWP 156: Operating doors	15/09/23	25/09/23



Number	Title	Issued	Effective
032 - 2023	TWP 100 Responsibilities of Train Crews	19/09/23	30/09/23
031 - 2023	Operation of Tangara trains fitted with ATP with Automatic Train Protection (ATP)	10/10/23	16/10/23
033 - 2023	Waratah (A and B SET) trains fitted with Automatic Train Protect equipment	17/10/23	23/10/23
034 - 2023	Testing Tangara trains fitted with ETCS Level 2	02/11/23	03/11/23
001 – 2024	TWP 182 Digital Train Radio	12/02/24	26/02/24
002 – 2024	Testing of a Millennium set (M31) with ETCS level 2 equipment	22/04/24	23/04/24
003 – 2024	Transition of NSW TrainLink Intercity Drivers and Guards to Sydney Trains	12/06/24	01/07/24
004 - 2024	Transfer and Testing of OSCAR Train (H5 set) with the Automatic Train Protection Protection(ATP) Trackside System	28/06/24	01/07/24
006 - 2024	TWP 152 Disabled trains	18/11/24	5/12/24



STATUS OF PERMANENT SAFE NOTICES

Number	Title	Issued	Effective
001 – 2025	Transition of NSW TrainLink Operations to Sydney Trains	19/12/24	01/01/25
004 - 2025	New Trackside Signage associated with Digital Systems Train Testing	23/02/25	23/02/25
007 - 2025	Use of Signal Key Switches	16/04/25	29/04/25
008 - 2025	Permanent Safe Notices Cancelled & Withdrawn in conjunction with Network Rules Amendments	16/04/2025	04/05/2025

Steve Swanson

Network Rules SpecialistTel:02 8922 4183 (external)2 4183 (internal)Email:stephen.swanson@transport.nsw.gov.au



STATUS OF NETWORK MANUALS AND FORMS

Network Manuals

Network Local Appendices	RailSafe Website	Online documents
Operator Specific Procedures	RailSafe Website	Online documents
Network Rules	RailSafe Website	Online documents
Network Procedures	RailSafe Website	Online documents
Forms	RailSafe Website	Online documents (or order as applicable)



weekly notice

Title

Status Sheet

Date issued

Train Working Procedures

TWP 100	TN 006 - 2021	April 2021
TWP 102	3	May 2012
TWP 108	4	May 2012
TWP 110	TN 009 - 2019	March 2019
TWP 112	TN 014 - 2020	August 2020
TWP 114	4	November 2015
TWP 116	3	May 2012
TWP 118	TN 004 - 2019	April 2019
TWP 120	3	May 2012
TWP 122	3	May 2012
TWP 124	TN 004 - 2020	May 2019
TWP 126	TN 005 - 2020	May 2019
TWP 128	3	May 2012
TWP 130	3	May 2012
TWP 132	3	May 2012
TWP 134	3	May 2012
TWP 136	TN 007 - 2019	March 2019
TWP 138	TN 017 - 2023	March 2023
TWP 142	3	May 2012
TWP 144	5	May 2012
TWP 146	3	May 2012
TWP 148	3	May 2012
TWP 150	TN 005 - 2017	April 2017
TWP 152	TN 016 - 2023	March 2023
TWP 154	TN 008 - 2018	July 2018
TWP 156	TN 011 - 2019	March 2019
TWP 158	3	May 2012
TWP 160	TN 005 - 2022	May 2022
TWP 162	TN 011- 2020	May 2019
TWP 164	4	May 2012
TWP 166	3	May 2012
TWP 168	3	May 2012
TWP 170	3	May 2012
TWP 172	4	May 2012
TWP 174	TN 004 - 2017	July 2017
TWP 176	TN 008 - 2017	July 2017
TWP 182	1	November 2015
TWP 188	1	November 2015
TWP 190	TN 008 - 2019	March 2019
TWP 192	TN 012 - 2019	March 2019



DISTRIBUTION OFFICERS

Sydney Trains

Safety and Environment

Maria Economou

Safety Support 2 4502 Maria.Economou@transport.nsw.gov.au

Train Crew Operations

Manager Day of Operations

8577 7029

Ð

TCOManagerDayofOperations@transport. nsw.gov.au

Train Crewing

Service Delivery Response

Megan Parker

Service Delivery Response 0491226502 megan.parker@transport.nsw.gov.au

Maintenance

Fleet Maintenance

Hoshedar Movdawalla

Fleet Maintenance Sydney Trains

Network Maintenance

Zaneta Janevski

Engineering & Maintenance 87570199 Ø zaneta.janevski@transport.nsw.gov.au

Dianna Di Giacomo

Engineering & Maintenance Administration Support

0478261139
 dianna.digiacomo@transport.nsw.gov.au_
 Eric Sugue
 Engineering & Maintenance

Materials Inspector 0447117499 Peric.surge@transport.nsw.gov.au

Shaun Smith Track Access Coordinator – North 0401710427 Shaun.smith@transport.nsw.gov.au

Bradley Stewart

Territory Planning Manager - Central Coast/Hamilton

Ennio Soster SCE Project Delivery Electrical 25236 25917 ENNIO.SOSTER@transport.nsw.gov.au

Adrian Aquilina Team leader - Strathfield Mains 97526610 adrian.aquilina@transport.nsw.gov.au

Christina Morgan Administration Support ICON 9379 6051 Christina.Morgan@transport.nsw.gov.au



Lorinda Melvin

Administration Support \$ 0439510480 Dirinda.melvin@transport.nsw.gov.au

Major Works

Greg Page

Infrastructure Track \$ 25375

Michael Warner

Signals and Electricity S 9848 9333 Dichael.warner@transport.nsw.gov.au

Logistics & Supply Chain

Murari Singh Contract Assurance Administrator Durari.Singh@transport.nsw.gov.au

Engineering & System Integrity

Yass Zahab

Geotechnical Services \$ 2 7589 2 7786 Passine.El-Zahab@transport.nsw.gov.au

Richard Agostino

C and CS 9 2137 8 2 0875 Richard.Agostino@transport.nsw.gov.au

Capability & Learning

Samantha Sheriff

Operations Trainer 6415822921 Samantha.Sherriff2@transport.nsw.gov.au

Peter Nilon

Survey Group S 9848 9904 peter.nilon@transport.nsw.gov.au

Lu Talevski

Administration Support – InterCity Sydney Trains

S 0459845723 Du.talevgski@transport.nsw.gov.au

NSW Trainlink

Brett Wunderlich

Operational Readiness & Standards Manager 0427458174 Brett.Wunderlich@transport.nsw.gov.au

Robert Blanch

Area Manager North Service Delivery



0419498494 ROBERT.BLANCH@transport.nsw.gov.au

Dwayne Purcell

Area Manager South Service Delivery 0428670850 Ð

DWAYNE.PURCELL@transport.nsw.gov.au

Suzanne Edwards Area Manager Central 0418271662

SUZANNE.EDWARDS@transport.nsw.gov.au







weekly notice

NOTES



NOTICE TO SUBSCRIBERS

The Weekly Notice is issued every Thursday and takes effect on the following Monday.

Those who require the Weekly Notice must ensure that they receive it and are aware of the changes that affect their work duties and responsibilities.

Director Network Standards, Systems & Quality

Sydney Trains

Level 4, 36-46 George Street Burwood NSW 2134 Thursday, 26 June 2025
