

27

weekly notice

Monday, 24 June 2024

Sunday, 30 June 2024

RailSafe





RailSafe

See online for all Safeworking Information

www.railsafe.org.au

Safeworking information, including Weekly Notices and SAFE Notices, is available on the RailSafe website.

By accessing Weekly Notices and SAFE Notices online, you will receive safety information more quickly. Weekly Notices remain on the RailSafe website for two years; Permanent and Temporary SAFE Notices remain online as long as they are current.

Anyone needing back issues of Weekly Notices and SAFE Notices should contact the Network Rules unit.

If you are outside Sydney Trains, you can reach the RailSafe website via the following address:

www.railsafe.org.au

Other Safeworking documents, such as Network Rules, Network Procedures, Network Local Appendices, Safeworking Policies, SafeTracks flyers, and contractor information are also available online.

**Director Safety and Standards
Sydney Trains**

Continued on next page

CONTENTS

<u>PUBLICATION DEADLINES AND SUBMISSION OF ARTICLES</u>	<u>4</u>
<u>WATERFALL (ILLAWARRA) – MTMS2 WATERFALL STABLING FACILITY PROJECT SIGNALLING FINAL WORKS</u>	<u>5</u>
<u>BANKSTOWN – INSTALLATION OF NEW SIGNAL ARRANGEMENTS (UNCOMMISSIONED / BAGGED)</u>	<u>26</u>
<u>CONISTON (ILLAWARRA) - UPGRADE 120 SIGNAL TO LED TYPE</u>	<u>27</u>
<u>STATUS OF TOM NOTICES</u>	<u>28</u>
<u>STATUS OF PERMANENT SAFE NOTICES</u>	<u>30</u>
<u>STATUS OF NETWORK MANUALS AND FORMS</u>	<u>31</u>
<u>DISTRIBUTION OFFICERS</u>	<u>33</u>

PUBLICATION DEADLINES AND SUBMISSION OF ARTICLES

Dates of the next four Weekly Notices and deadlines for articles are:

<i>Weekly Notice</i>	<i>For Week</i>	<i>Deadline</i>
28	01/07/2024 – 07/07/2024	28/05/2024
29	08/07/2024 – 14/07/2024	04/06/2024
31	15/07/2024 – 21/08/2024	11/06/2024

To meet printing and distributing schedules, articles for a Weekly Notice must be received by its deadline.

Articles submitted after a deadline will be published in the next issue of the Weekly Notice. This may result in information not being distributed in time for it to be acted upon.

When submitting articles, please include your name, position title, telephone numbers and email address at the end of the articles as shown below:

Steve Swanson

Network Rules Specialist

Tel: 02 8922 4183 (external) 2 4183 (internal)

Email: stephen.swanson@transport.nsw.gov.au

WATERFALL (ILLAWARRA) – MTMS2 WATERFALL STABLING FACILITY PROJECT SIGNALLING FINAL WORKS

Commencing at **0200 hours** on **Saturday, 06 July 2024**, and continuing until **0200 hours** on **Monday, 15 July 2024**, the following work will be carried out:

Temporary Arrangements

At the commencement of the possession, the Waterfall Relay Interlocking and Signal Box at Waterfall Station will be decommissioned. The Down Main and Down Refuge Loop will be made operational for down direction movements and the Up Main, Up Refuge Loop and No.2 Up Sidings will be made operational for up direction movements using Pilot Staff Working (PSW) between Monday 08 July 2024 to Saturday 13 July 2024. The scheduled times for the up and down movements are detailed in STN 1104-2024.

During the PSW period, all points through the remodelled area will be spiked, clipped and XL locked in the appropriate position required for the Pilot Staff Working.

New Arrangements

A new track configuration will be brought into use between the Main Lines, Up Sidings, Up Goods Loop, Up Refuge Loop and Perway Siding. The existing Up Goods Loop will be extended towards Sydney to accommodate 1500m long freight trains. No.1 Up Siding and No. 2 Up Siding will provide a new stabling facility suitable for 10 x 8-car electric Suburban trains on the T4 Illawarra. Installation of new crossovers, turnouts, and catchpoints to facilitate entry/exit to/from the new stabling facility. The Up Goods Loop and Perway Siding will not be available for electric traction.

The Sydney end of Platform 1 and 2 will be extended approx. 45m to accommodate new 10 car NIF trains with the following platform car marker changes,

- Installation of a “10” car marker on the Platform 1 Sydney end fenceline and
- Installation of a “10” car marker on Platform 2 Sydney end, approx. 4.14m from the fenceline with an additional post mounted “10” car marker located in the cess at the same chainage.
- Relocation of the “8” car marker on Platform 2 Sydney end approx. 10m towards Sydney.

New post mounted “8” Car Marker sign on the Up Main located at approx. 37.157km.

New signals, trainstops, points and signage will be installed as detailed. At the conclusion of the possession, remote control of the new Microlok II Waterfall Interlocking will be from the Sutherland Panel at the ROC via the Sydenham RCS.

A Drivers Diagram showing the new arrangements appears in this Weekly Notice.

Line side Infrastructure Alterations

The following tables summarise all signals, signs, berths, points and guard's indicators within the resignalled area. Refer also to the Drivers Diagram for the new arrangements.

Signals

Signal	Route	Designation	Route Indication	Remarks
WL1 (OLD W79)	(M)	Down Main	-	Existing signal renamed. New Medium indication provided. Turnout Repeater brought into use. Existing YL/EYL signs retained.
WL3 (OLD W1)	(M)A	Down Main to Down Refuge Loop	LH BOL	Existing signal renamed. New Caution Turnout and Medium Turnout indications provided. New Right-Hand BOL brought into use. New (M/S)C route provided.
	(M)B	Down Main	-	
	(M)C	Down Main to Up Main	RH BOL	
	(S)A	Shunt, Down Main to Down Refuge Loop	DR	
	(S)B	Shunt, Down Main	DM	
WL5	(S)C	Shunt, Down Main to Up Main	UM	New shunt signal.
	(S)A	Shunt, Up Main	UM	
WL5	(S)B	Shunt, Up Main to Up Goods Loop	UG	New shunt signal.
	(S)A	Shunt, Up Main	UM	
WL6	(M)	Up Main	-	New signal and trainstop.

Signal	Route	Designation	Route Indication	Remarks
	(S)	Shunt, Up Main	-	
WL8	(M)	Up Goods Loop to Up Main	-	New signal and trainstop.
	(S)	Shunt, Up Goods Loop to Up Main	-	
WL17	(M)	Down Main	-	New signal and trainstop.
WL19	(M)A	Up Main	-	New signal on RHS of line. New trainstop.
	(S)A	Shunt, Up Main	UM	
	(S)B	Shunt, Up Main to No. 1 Up Siding	S1	
	(S)C	Shunt, Up Main to No. 2 Up Siding	S2	
WL20	(M)	Up Main	-	New signal and trainstop.
	(S)	Shunt, Up Main	-	
WL22	(M)	Up Siding to Up Main	RH BOL	New signal and trainstop.
	(S)	Shunt, Up Siding to Up Main		Approach cleared by train on berth track. Flashing green repeater until WL24 or WL26 route used or train on berth track.
WL24	(S)	No.1 Up Siding	-	New signal and trainstop. Requires WL22 route set.
WL26	(S)	Shunt, No.1 Up Siding	-	New signal and trainstop. Requires WL22 route set.

Signal	Route	Designation	Route Indication	Remarks
WL28	(M)	Up Goods	-	New signal and trainstop.
WL34	(M)	Up Main	-	New signal and trainstop.
WL35	(M)	Down Refuge Loop	-	New signal and trainstop.
WL37	(M)A	Down Main	-	New signal and trainstop.
	(M)B	Down Main to Up Main	RH BOL	
	(S)A	Shunt, Down Main	DM	
	(S)B	Shunt, Down Main to Up Main	UM	
WL39	(M)A	Up Main to Down Main	LH BOL	New Signal on RHS of line. 39(M) routes oversets 45(S). New trainstop.
	(M)B	Up Main	-	
	(M)C	Up Main to Up Refuge Loop	RH BOL	
	(S)	Shunt, Up Main	-	
WL45 (OLD 9)	(S)A	Shunt, Up Main to Down Main	DM	Existing signal renamed. Overset by 39(M) routes Green aspect provided. New (S)C route provided.
	(S)B	Shunt, Up Main	UM	
			Green Light	
(S)C	Shunt, Up Main to Up Refuge Loop	UR		
WL47	(S)	Shunt, No.1 Up Siding to Up Refuge Loop	-	New signal and trainstop.

Signal	Route	Designation	Route Indication	Remarks
WL49	(S)	Shunt, No.2 Up Siding to Up Refuge Loop	-	New signal and trainstop.
WL51	(S)A	Shunt, Up Goods Loop	UG	New signal.
	(S)B	Shunt, Perway Siding	PS	
WL52	(M)	Up Refuge Loop to Up Main	-	New signal and trainstop.
	(S)	Shunt, Up Refuge Loop to Up Main	-	
WL54	(S)	Shunt, Perway Siding to Up Goods Loop	-	New signal.
WL60 (OLD W12)	(M)A	Down Main to Up Main	LH BOL	Existing signal renamed.
	(S)A	Shunt, Down Main to Up Main	UM	New Medium Turnout indication provided. New route indicator provided.
WL62 (OLD W10)	(M)	Up Main	-	Existing signal renamed.
	(S)	Shunt, Up Main	-	
WL63 (OLD 33)	(S)	Shunt, No. 3 Down Siding to Down Refuge Loop	-	Existing signal renamed.
WL65 (OLD 35)	(S)	Shunt, No. 2 Down Siding to Down Refuge Loop	-	Existing signal renamed.

Signal	Route	Designation	Route Indication	Remarks
WL67 (OLD 37)	(S)	Shunt, No. 1 Down Siding to Down Refuge Loop	-	Existing signal renamed.
WL69 (OLD W39)	(M)B	Down Refuge Loop to Down Main	RH BOL	Existing signal renamed. New Medium Turnout indication provided. 69(M)B route oversets 83(S)B
	(S)	Shunt, Down Refuge Loop	-	
WL70	(S)A	Shunt, Up Refuge Loop to No.2 Up Siding	S2	New signal. 70(S)C Overset by 86(M)B or 88(M)B routes. Green aspect provided.
	(S)B	Shunt, Up Refuge Loop to No.1 Up Siding	S1	
	(S)C	Shunt, Up Refuge Loop	UR GREEN LIGHT	
WL71	(M)B	Up Goods Loop to Down Main	LH BOL	New signal and trainstop.
	(M)C	Up Goods Loop to Up Main	-	
	(S)A	Shunt, Up Goods Loop to Shunting Neck	S	
	(S)B	Shunt, Up Goods Loop to Down Main	DM	
	(S)C	Shunt, Up Goods Loop to Up Main	UM	
WL73	(M)B	Up Refuge Loop to Down Main	LH BOL	

Signal	Route	Designation	Route Indication	Remarks
(OLD W23)	(M)C	Up Refuge Loop to Up Main	-	Existing signal renamed. New Medium Turnout indication provided. Shunt route indicator brought into use. New shunt routes provided.
	(S)A	Shunt, Up Refuge Loop to Shunting Neck	S	
	(S)B	Shunt, Up Refuge Loop to Down Main	DM	
	(S)C	Shunt, Up Refuge Loop to Up Main	UM	
WL73 CO-ACT (OLD W23 CO-ACT)	(M)B	Up Refuge Loop to Down Main	D	Existing signal renamed. New shunt routes provided. New pulsating yellow aspect provided.
	(M)C	Up Refuge Loop to Up Main	U	
	(S)A	Shunt, Up Refuge Loop to Shunting Neck	S	
	(S)B	Shunt, Up Refuge Loop to Down Main	D	
	(S)C	Shunt, Up Refuge Loop to Up Main	U	
WL74 (OLD 18)	(S)A	Shunt, Down Refuge Loop	DR	Existing signal renamed.
	(S)B	Shunt, Down Refuge Loop to Down Siding	DS	
WL76 (OLD 34)	(S)A	Shunt, Up Refuge Loop to Up Goods Loop	UG	Existing signal renamed. (S)A route brought into use.

Signal	Route	Designation	Route Indication	Remarks
	(S)B	Shunt, Up Refuge Loop	UR GREEN LIGHT	76(S)A Overset by 86(M)A or 88(M)A routes. 76(S)B Overset by 86(M)B or 88(M)B routes. Green aspect provided
WL77 (OLD W17)	(M)B	Down Main	-	Existing signal renamed.
	(S)A	Shunt, Down Main to Shunting Neck	S	
	(S)B	Shunt, Down Main	DM	
WL77 CO-ACT (W17 CO-ACT)	(M)B	Down Main	-	Existing signal renamed.
	(S)A	Shunt, Down Main to Shunting Neck	S	
	(S)B	Shunt, Down Main	M	
WL79 (OLD W19)	(M)B	Up Main to Down Main	LH BOL	Existing signal renamed. New Medium Turnout indication provided.
	(M)C	Up Main	-	
	(S)A	Shunt, Up Main to Shunting Neck	S	
	(S)B	Shunt, Up Main to Down Main	DM	
	(S)C	Shunt, Up Main	UM	
WL79 CO-ACT	(M)B	Up Main to Down Main	LH BOL	Existing signal renamed. New Medium Turnout indication provided.
	(M)C	Up Main	-	

Signal	Route	Designation	Route Indication	Remarks
(W19 CO-ACT)	(S)A	Shunt, Up Main to Shunting Neck	S	
	(S)B	Shunt, Up Main to Down Main	DM	
	(S)C	Shunt, Up Main	UM	
WL83 (OLD 13)	(S)A	Shunt, Down Refuge Loop to Shunting Neck	S	Existing signal renamed. Overset by 69(M)B route.
	(S)B	Shunt, Down Refuge Loop to Down Main	DM	
WL84 (OLD 24)	(S)A	Shunt, Shunting Neck to Up Refuge Loop	UR	Existing signal renamed.
	(S)B	Shunt, Shunting Neck to Up Main	UM	
	(S)C	Shunt, Shunting Neck to Down Main	DM	
	(S)D	Shunt, Shunting Neck to Down Refuge Loop	DR	
WL86 (OLD W20)	(M)A	Down Main to Up Goods Loop	LH BOL + 'G'	Existing signal renamed. New Left-Hand Turnout Repeater provided. New Low Speed indication provided. New Medium indication provided.
	(M)B LSp	Down Main to Up Refuge Loop	UR	
	(M)B	Down Main to Up Refuge Loop	LH BOL + 'R'	

Signal	Route	Designation	Route Indication	Remarks
	(M)C	Down Main to Up Main	LH BOL + 'U'	New Medium Turnout indication provided. 86(M)A route oversets 76(S)A. 86(M)B route oversets 76(S)B and 70(S)C.
	(M)D	Down Main	-	
	(S)B	Shunt, Down Main to Up Refuge Loop	UR	
	(S)C	Shunt, Down Main to Up Main	UM	
	(S)D	Shunt, Down Main	DM	
	(S)E	Shunt, Down Main to Down Refuge Loop	DR	
WL88 (OLD W22)	(M)A	Up Main to Up Goods Loop	LH BOL + 'G'	Existing signal renamed. New Low Speed indication provided. New Medium Turnout indication provided. 88(M)A route oversets 76(S)A. 88(M)B route oversets 76(S)B and 70(S)C.
	(M)B LSp	Up Main to Up Refuge Loop	UR	
	(M)B	Up Main to Up Refuge Loop	LH BOL + 'R'	
	(M)C	Up Main	-	
	(S)B	Shunt, Up Main to Up Refuge Loop	UR	
	(S)C	Shunt, Up Main	UM	
WL91D (OLD W25D)	(M)	Down Main	-	Existing signal renamed. Flashing green repeater until accepted by Helensburgh WG781

Signal	Route	Designation	Route Indication	Remarks
WL93U (OLD W27U)	(M)	Up Main	-	Existing signal renamed. Flashing green repeater until accepted by Helensburgh WG781
WL94D (OLD W28D)	(M)	Down Main	-	Existing signal renamed. New Left-Hand Turnout Repeater and medium indication provided. Existing YL/EYL signs retained.
WL96U (OLD W26U)	(M)	Up Main	-	Existing signal renamed. New Left-Hand Turnout Repeater provided. Existing YL/EYL signs retained.
W3	(M)A	Down Main	-	Signal and trainstop removed.
	(M)B	Down Main to Up Main	RH BOL + 'U'	
	(M)C	Down Main to Up Refuge Loop	RH BOL + 'R'	
	(M)D	Down Main to Up Goods Loop	R/H BOL + 'G'	
	(S)	Shunt, Down Main	-	
W4	(M)C	Up Refuge Loop to Up Main	-	Signal and trainstop removed.
	(S)A	Shunt, Up Refuge Loop to No. 2 Loco Exchange	2L	
	(S)B	Shunt, Up Refuge Loop to No. 1 Loco Exchange	1L	
	(S)C	Shunt, Up Refuge Loop to Up Main	UM	

Signal	Route	Designation	Route Indication	Remarks
	(S)D	Shunt, Up Refuge Loop to Down Main	DM	
W5	(M)A	Down Refuge Loop	-	Signal and trainstop removed.
	(M)B	Down Refuge Loop to Down Main	RH BOL + 'D'	
	(M)C	Down Refuge Loop to Up Main	RH BOL + 'U'	
	(M)D	Down Refuge Loop to Up Refuge Loop	R	
	(M)E	Down Refuge Loop to Up Goods Loop	G	
	(S)A	Shunt, Down Refuge Loop	DR	
	(S)B	Shunt, Down Refuge Loop to Down Main	DM	
W6	(M)	Up Main	-	Signal and trainstop removed.
	(S)A	Shunt, Up Main	UM	
	(S)B	Shunt, Up Main to Down Main	DM	
W7	(M)	Down Main	-	Signal and trainstop removed.
	(S)	Shunt, Down Main	-	
8	(S)	Shunt, Down Refuge Loop	-	Signal removed.
11	A	Down Main	D	Signal removed

Signal	Route	Designation	Route Indication	Remarks
	B	Down Main to Up Main	U	
	C	Down Main to Up Refuge Loop	R	
	D	Down Main to Up Goods Loop	G	
		Green Light	•	
14	(S)	Down Refuge Loop	-	Signal removed.
15	A	Up Main	U	Signal removed.
	B	Up Main to Up Refuge Loop	R	
	C	Up Main to Up Goods Loop	G	
41	A	Up Refuge Loop to Shunting Neck	S	Signal removed.
	B	Up Refuge Loop to Down Main	D	
	C	Up Refuge Loop to Up Main	U	

Points (Refer to Drivers Diagram for positioning of EOL/ESML)

Points Number	Designation	Emergency	
		Operation	Remarks
Points			
WL301A/B (OLD 47A/B)	50km/h Turnout and Catchpoint Down Main to Down Refuge Loop	EOL	Existing Turnout and Catchpoint renamed

Points Number	Designation	Emergency	
		Operation Points	Remarks
WL302A/B	60km/h Turnout and Catchpoint Up Main to Up Goods Loop	EOL	Siemens D84M MKIII point machines utilising an in bearer Spherolock arrangement was previously installed, clipped and XL locked normal, brought into normal operational use.
WL304A/B	45km/h Crossover Down Main to Up Main	EOL	Siemens D84M MKIII point machines utilising an in bearer Spherolock arrangement was previously installed, clipped and XL locked normal, brought into normal operational use.
WL305A/B	35km/h Crossover Up Main to No.1 Up Siding	EOL	Siemens D84M MKIII point machines utilising an in bearer Spherolock arrangement was previously installed, clipped and XL locked normal, brought into normal operational use.
WL307	25km/h Crossover No.1 Up Siding to No.2 Up Siding	EOL	Siemens D84M MKIII point machine utilising an in bearer Spherolock arrangement was previously installed, brought into normal operational use.
WL310A/B (OLD 54(310)A/B)	45km/h Crossover Down Main to Up Main	EOL	Existing Crossover renamed.
WL311A/B	45km/h Turnout and Catchpoint Up Refuge Loop to Up Main	EOL	Siemens D84M MKIII point machines utilising an in bearer Spherolock arrangement was previously installed, clipped and XL locked normal, brought into normal operational use.
WL312A/B	35km/h Crossover Down Main to Up Main	EOL	Siemens D84M MKIII point machines utilising an in bearer Spherolock arrangement was previously installed, clipped and XL locked normal, brought into normal operational use.

Points Number	Designation	Emergency	
		Operation Points	Remarks
WL315A/B	25km/h Turnout and Catchpoint Up Goods Loop to Perway Siding	EOL	New Siemens D84M MKIII point machines utilising an in bearer Spherolock arrangement
WL316	25km/h Turnout No.2 Up Siding to No.1 Up Siding	EOL	Siemens D84M MKIII point machine utilising an in bearer Spherolock arrangement was previously installed, clipped and XL locked reverse, brought into normal operational use.
WL317A/B	25km/h Turnout and Catchpoint Up Refuge Loop to No.2 Up Siding	EOL	Siemens D84M MKIII point machines utilising an in bearer Spherolock arrangement was previously installed, clipped and XL locked reverse, brought into normal operational use.
WL318A/B (OLD 60A/B)	45km/h Turnout and Catchpoint Up Refuge Loop to Up Goods Loop	EOL	Existing Turnout and Catchpoint renamed. Previously installed, clipped and XL locked normal, brought into normal operational use.
WL320A/B/C (OLD 61A/B/C)	25km/h Turnout and Derailers Down Refuge Loop to Down Siding	ESML	Existing 61A/B/C Turnout and Derailers renamed WL320A/B/C.
WL321A/B (OLD 57A/B)	50km/h Turnout and Catchpoint Up Main to Up Refuge Loop	EOL	Existing Turnout and Catchpoint renamed.

Points Number	Designation	Emergency	
		Operation Points	Remarks
WL322A/B (OLD 56A/B)	25km/h Crossover Down Refuge Loop to Down Main	EOL	Existing Crossover renamed.
WL323A/B (OLD 58A/B)	25km/h Crossover Down Main to Up Main	EOL	Existing Crossover renamed.
WL324A/B (OLD 59A/B)	25km/h Crossover Shunting Neck to Down Main	EOL	Existing Crossover renamed.
WL325A/B (OLD 63A/B)	25km/h Catchpoint Shunting Neck	EOL	Existing Catchpoints renamed.
46	Catchpoint Up Refuge Loop	ESML	Existing HW4400 point machine and ESML removed.
51A/B	25km/h Crossover Down Main to Up Main	EOL	Existing D84M point machines and EOL removed.
52A/B	50km/h Crossover Up Refuge Loop to Up Main	ESML	Existing M3A MKIII point machines and ESML removed.

Stabling Berths: All Stabling Berths are Bidirectional

Stabling Berth	Length (approx..)	Remarks
A	176m	No.1 Up Siding

Stabling Berth	Length (approx.)	Remarks
B	168m	No.1 Up Siding
C	168m	No.1 Up Siding
D	168m	No.1 Up Siding
E	178m	No.1 Up Siding
F	177m	No.2 Up Siding
G	168m	No.2 Up Siding
H	168m	No.2 Up Siding
J	168m	No.2 Up Siding
K	178m	No.2 Up Siding
Berth signage is provided marking the berth limits, installed on the adjacent signal or adjacent wheel sensor.		

Perway Siding

A new buffer stop light will be installed, mounted on the buffer stop, at the end of Perway siding which is 145m in length.

Guard's Indicators

Guard Indicators	Designation	Remarks
60 GI (OLD 12)	Waterfall Platform 2, Down Main Up Direction	2 x existing guard's indicators operating in conjunction with WL60 Signal
62 GI (OLD 10)	Waterfall Platform 1, Up Main Up Direction	2 x existing guard's indicators operating in conjunction with WL62 Signal
77 GI (OLD 17)	Waterfall Platform 2, Down Main Down Direction	2 x existing guard's indicators operating in conjunction with WL77 Signal
79 GI (OLD 19)	Waterfall Platform 1, Up Main Down Direction	2 x existing guard's indicators operating in conjunction with WL79 Signal

Intermediate Trainstops

Intermediate Trainstop	Designation	Remarks
WL86/88 ITS1	Up Refuge Loop	Up Direction Speed 25km/h 9 Seconds on 73AT track with 318 points normal
WL86/88 ITS2	Up Refuge Loop	Up Direction Speed 10km/h 24 Seconds on URBT track with 317 points normal

Axle Counter Resets

Within No.1 and No.2 Up Siding and Perway Siding axle counters provide the Rail Vehicle Detection. In certain situations, the axle counter track sections require resetting.

Trackside reset facilities have been provided as per the table below and is to be used in conjunction with the reset enable functionality provided on the signaller's workstation.

Trackside Axle Counter Reset	Applicable Line	Location (approx.)	Remarks
US1GT/USHT	No.1 Up Siding	Adjacent to WL24 signal	Local Reset US1GT or USHT track sections.
US1FT/US1DT	No.1 Up Siding	Adjacent to B/C berth sign	Local Reset US1DT or US1FT track sections.
US1CT/US1BT	No.1 Up Siding	Adjacent to D/E berth sign	Local Reset US1BT or US1CT track sections.
US2BT/USAT	No.2 Up Siding	Adjacent to WL49 signal	Local Reset USAT or US2BT track sections.
US2DT/US2CT	No.2 Up Siding	Adjacent to J/H berth sign	Local Reset US2DT or US2CT track sections.
US2GT/US2FT	No.2 Up Siding	Adjacent to G/F berth sign	Local Reset US2GT or US2FT track sections.
GLAT(2)	Up Goods Loop / Perway Siding	Adjacent to 315A points	Local Reset GLAT(2) track section.

In addition, a Preparatory Reset / Sweep Control function is provided on the signaller's workstation for GLAT(2) track however it will be booked out of use and not available.

Instructions and requirements for resetting axle counters will be detailed in the Network Local Appendix NLA 412 and the Signalling Safeworking procedures.

Signage

Sign	Location (approx..)	Remarks
'END SIGNALLED AUTHORITY – DO NOT PROCEED UNLESS AUTHORIZED'	Adjacent to WL320A points	Up Direction on RHS of line – Down Sidings
Electric Train Stop	Adjacent to WL302A points	Down Direction on RHS of line – Up Goods Loop Unwired
Pantograph Down	Adjacent to WL5 signal	Down Direction on RHS of line – Up Goods Loop Unwired
Electric Train Stop	Adjacent to WL318B points	Up Direction on LHS of line – Up Goods Loop Unwired
Pantograph Down	Adjacent to WL76 signal	Up Direction on LHS of line – Up Goods Loop Unwired
Point Cleared 8 Cars	City side of WL19 signal	Up Direction on LHS of line – Up Main
Point Cleared 8 Cars	Between WL39 and WL34 signal	Up Direction on LHS of line – Up Main
Point Cleared 10 Cars	Between WL39 and W34 signal	Up Direction on LHS of line – Up Main
Safety Overrun Area No Rolling Stock or Equipment to Be Left Here	Centre line of WL305B points run off track	Up Direction within 4 foot – No.1 Up Siding
Yard 13 Speed	Adjacent to WL307 points	Down Direction on LHS of line – No.1 Up Siding

Sign	Location (approx..)	Remarks
Yard 13 Speed	Adjacent to WL317A points	Up Direction on LHS of line – No.2 Up Siding
Advisory 10 Speed	Adjacent to WL317B points	Up Direction on LHS of line – Up Refuge Loop
Shunting Limit	Behind of WL69 signal	Up Direction on LHS of line – Down Refuge Loop

Temporary Stop Block

Location(approx..)	Designation	Remarks
36.937km Adjacent to WL302B points	Up Good Loop	Temporary Stop Block removed
37.743km Adjacent to 52B points	No.1 Up Siding	Temporary Stop Block removed
38.476km Adjacent to WL316 points	No.2 Up Siding	Temporary Stop Block removed
38.588km Adjacent to WL317B points	Up Refuge Loop	Temporary Stop Block removed

Helensburgh Up and Down Main Accept controls

The Helensburgh Up Accept controls W44 and W42 will be renamed to WL100 and WL98.

Telephones

Telephones will be provided adjacent to the EOL locations and Axle Counter reset boxes as shown on the Drivers Diagram. All new and retained phones will be arranged to call the area controller for Sutherland Panel.

VER06032024**Diagram VER06032024****Adam Toffolo**

Signalling Commissioning Engineer, JMDR

Mob: 0416 942 861

Email: adam.toffolo@jmdr.com

Joe Trinh


Design Delivery Manager, JMDR

Mob: 0411566162

Email: joe.trinh@jmdr.com

SIGNAL	ROUTE	DESTINATION	INDICATION	TYPE
3	3(M)A	DOWN REFUGE	DR	BOL
	3(M)B	DOWN MAIN	-	-
	3(M)C	UP MAIN	UM	BOL
	3(S)A	DOWN REFUGE	DR	SRI
	3(S)B	DOWN MAIN	DM	SRI
	3(S)C	UP MAIN	UM	SRI

3(S)	A	DR	UM	C
	B	DM		

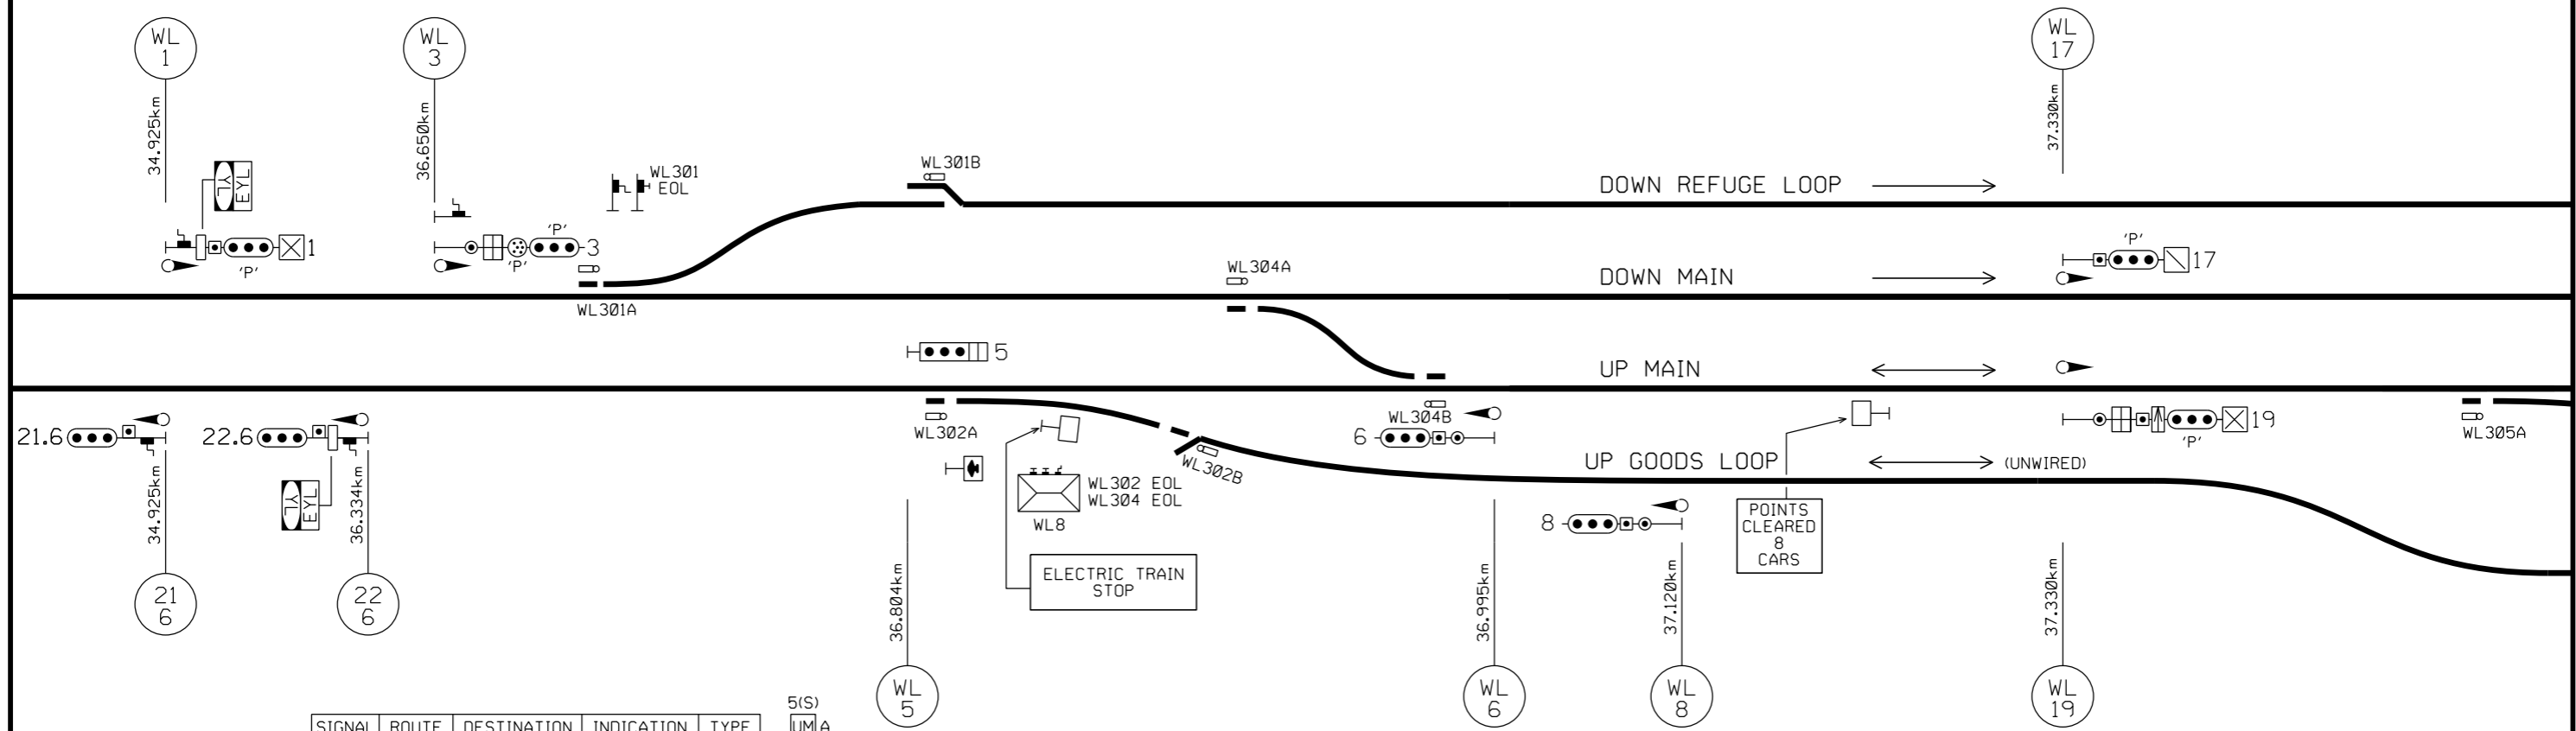

SIGNAL	ROUTE	DESTINATION	INDICATION	TYPE
5	5(S)A	UP MAIN	UM	SRI
	5(S)B	UP GOODS	UG	SRI

5(S)	A	UM
	B	UG

SIGNAL	ROUTE	DESTINATION	INDICATION	TYPE
19	19(M)	UP MAIN	-	-
	19(S)A	UP MAIN	UM	SRI
	19(S)B	No.1 UP SIDING	S1	SRI
	19(S)C	No.2 UP SIDING	S2	SRI

19(S)	A	UM	S2	C
	B	S1		



Transport for NSW

WATERFALL

MTMS2 WATERFALL STABLING FACILITY JULY 2024
DRIVERS DIAGRAM SHEET 1 OF 4


Produced by JMDR

VER. 06032024


SIGNAL	ROUTE	DESTINATION	INDICATION	TYPE
22	22(M)	UP MAIN	.	BOL
	22(S)	UP MAIN	-	-

SIGNAL	ROUTE	DESTINATION	INDICATION	TYPE
37	37(M)A	DOWN MAIN	-	-
	37(M)B	UP MAIN	.	BOL
	37(S)A	DOWN MAIN	DM	SRI
	37(S)B	UP MAIN	UM	SRI

SIGNAL	ROUTE	DESTINATION	INDICATION	TYPE
39	39(M)A	DOWN MAIN	.	BOL
	39(M)B	UP MAIN	-	-
	39(M)C	UP REFUGE	.	BOL
	39(S)	UP MAIN	-	-

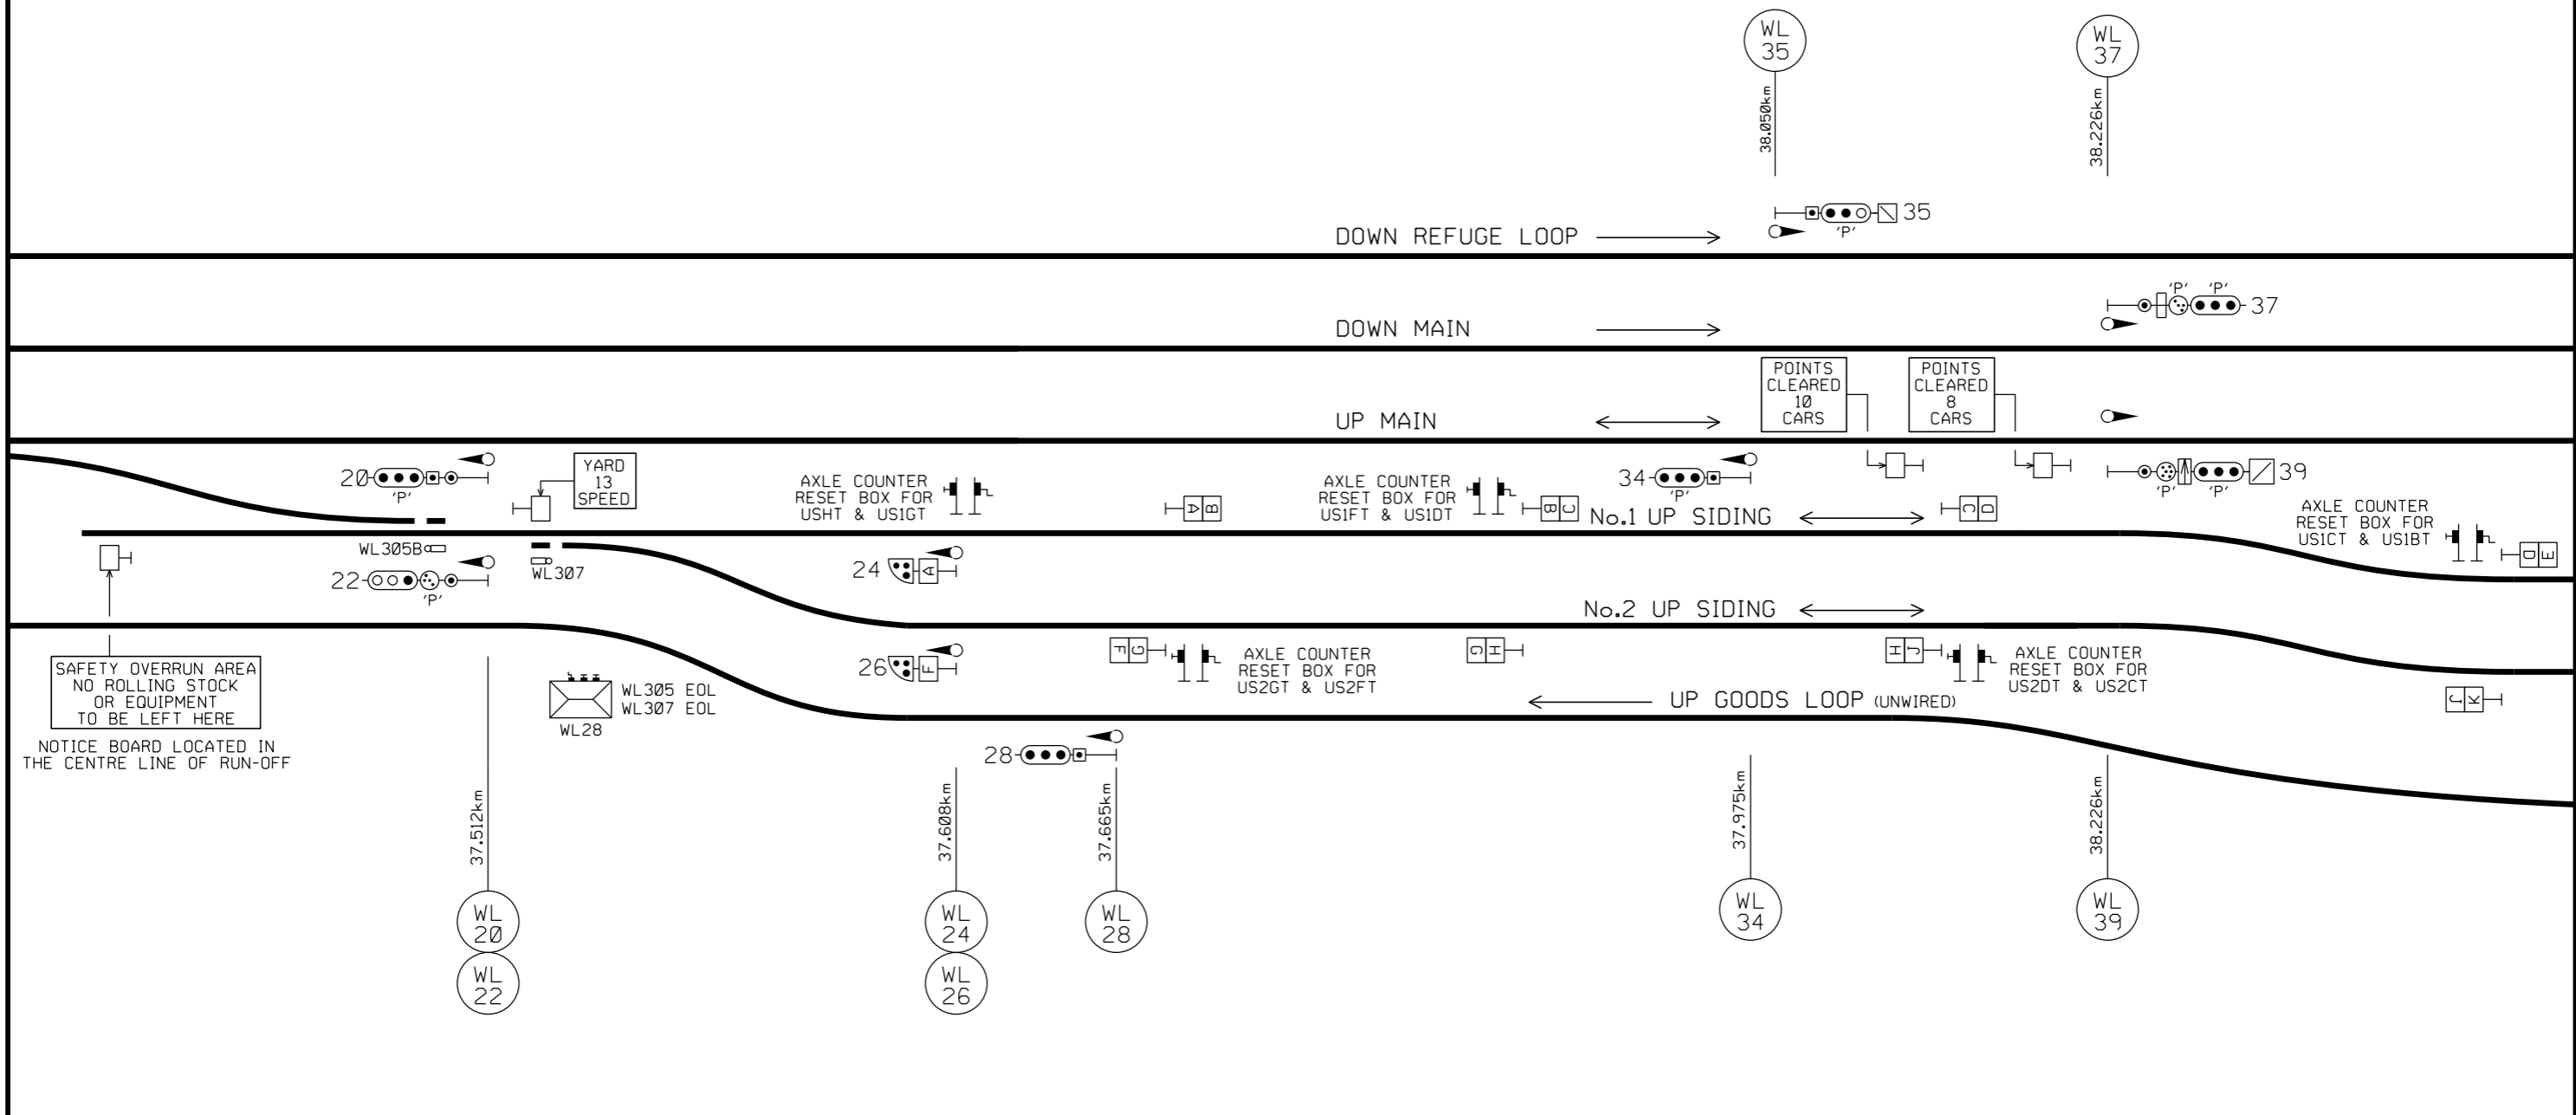

WATERFALL
 MTMS2 WATERFALL STABLING FACILITY JULY 2024
 DRIVERS DIAGRAM SHEET 2 OF 4
 Produced by JMDR
 VER. 06032024

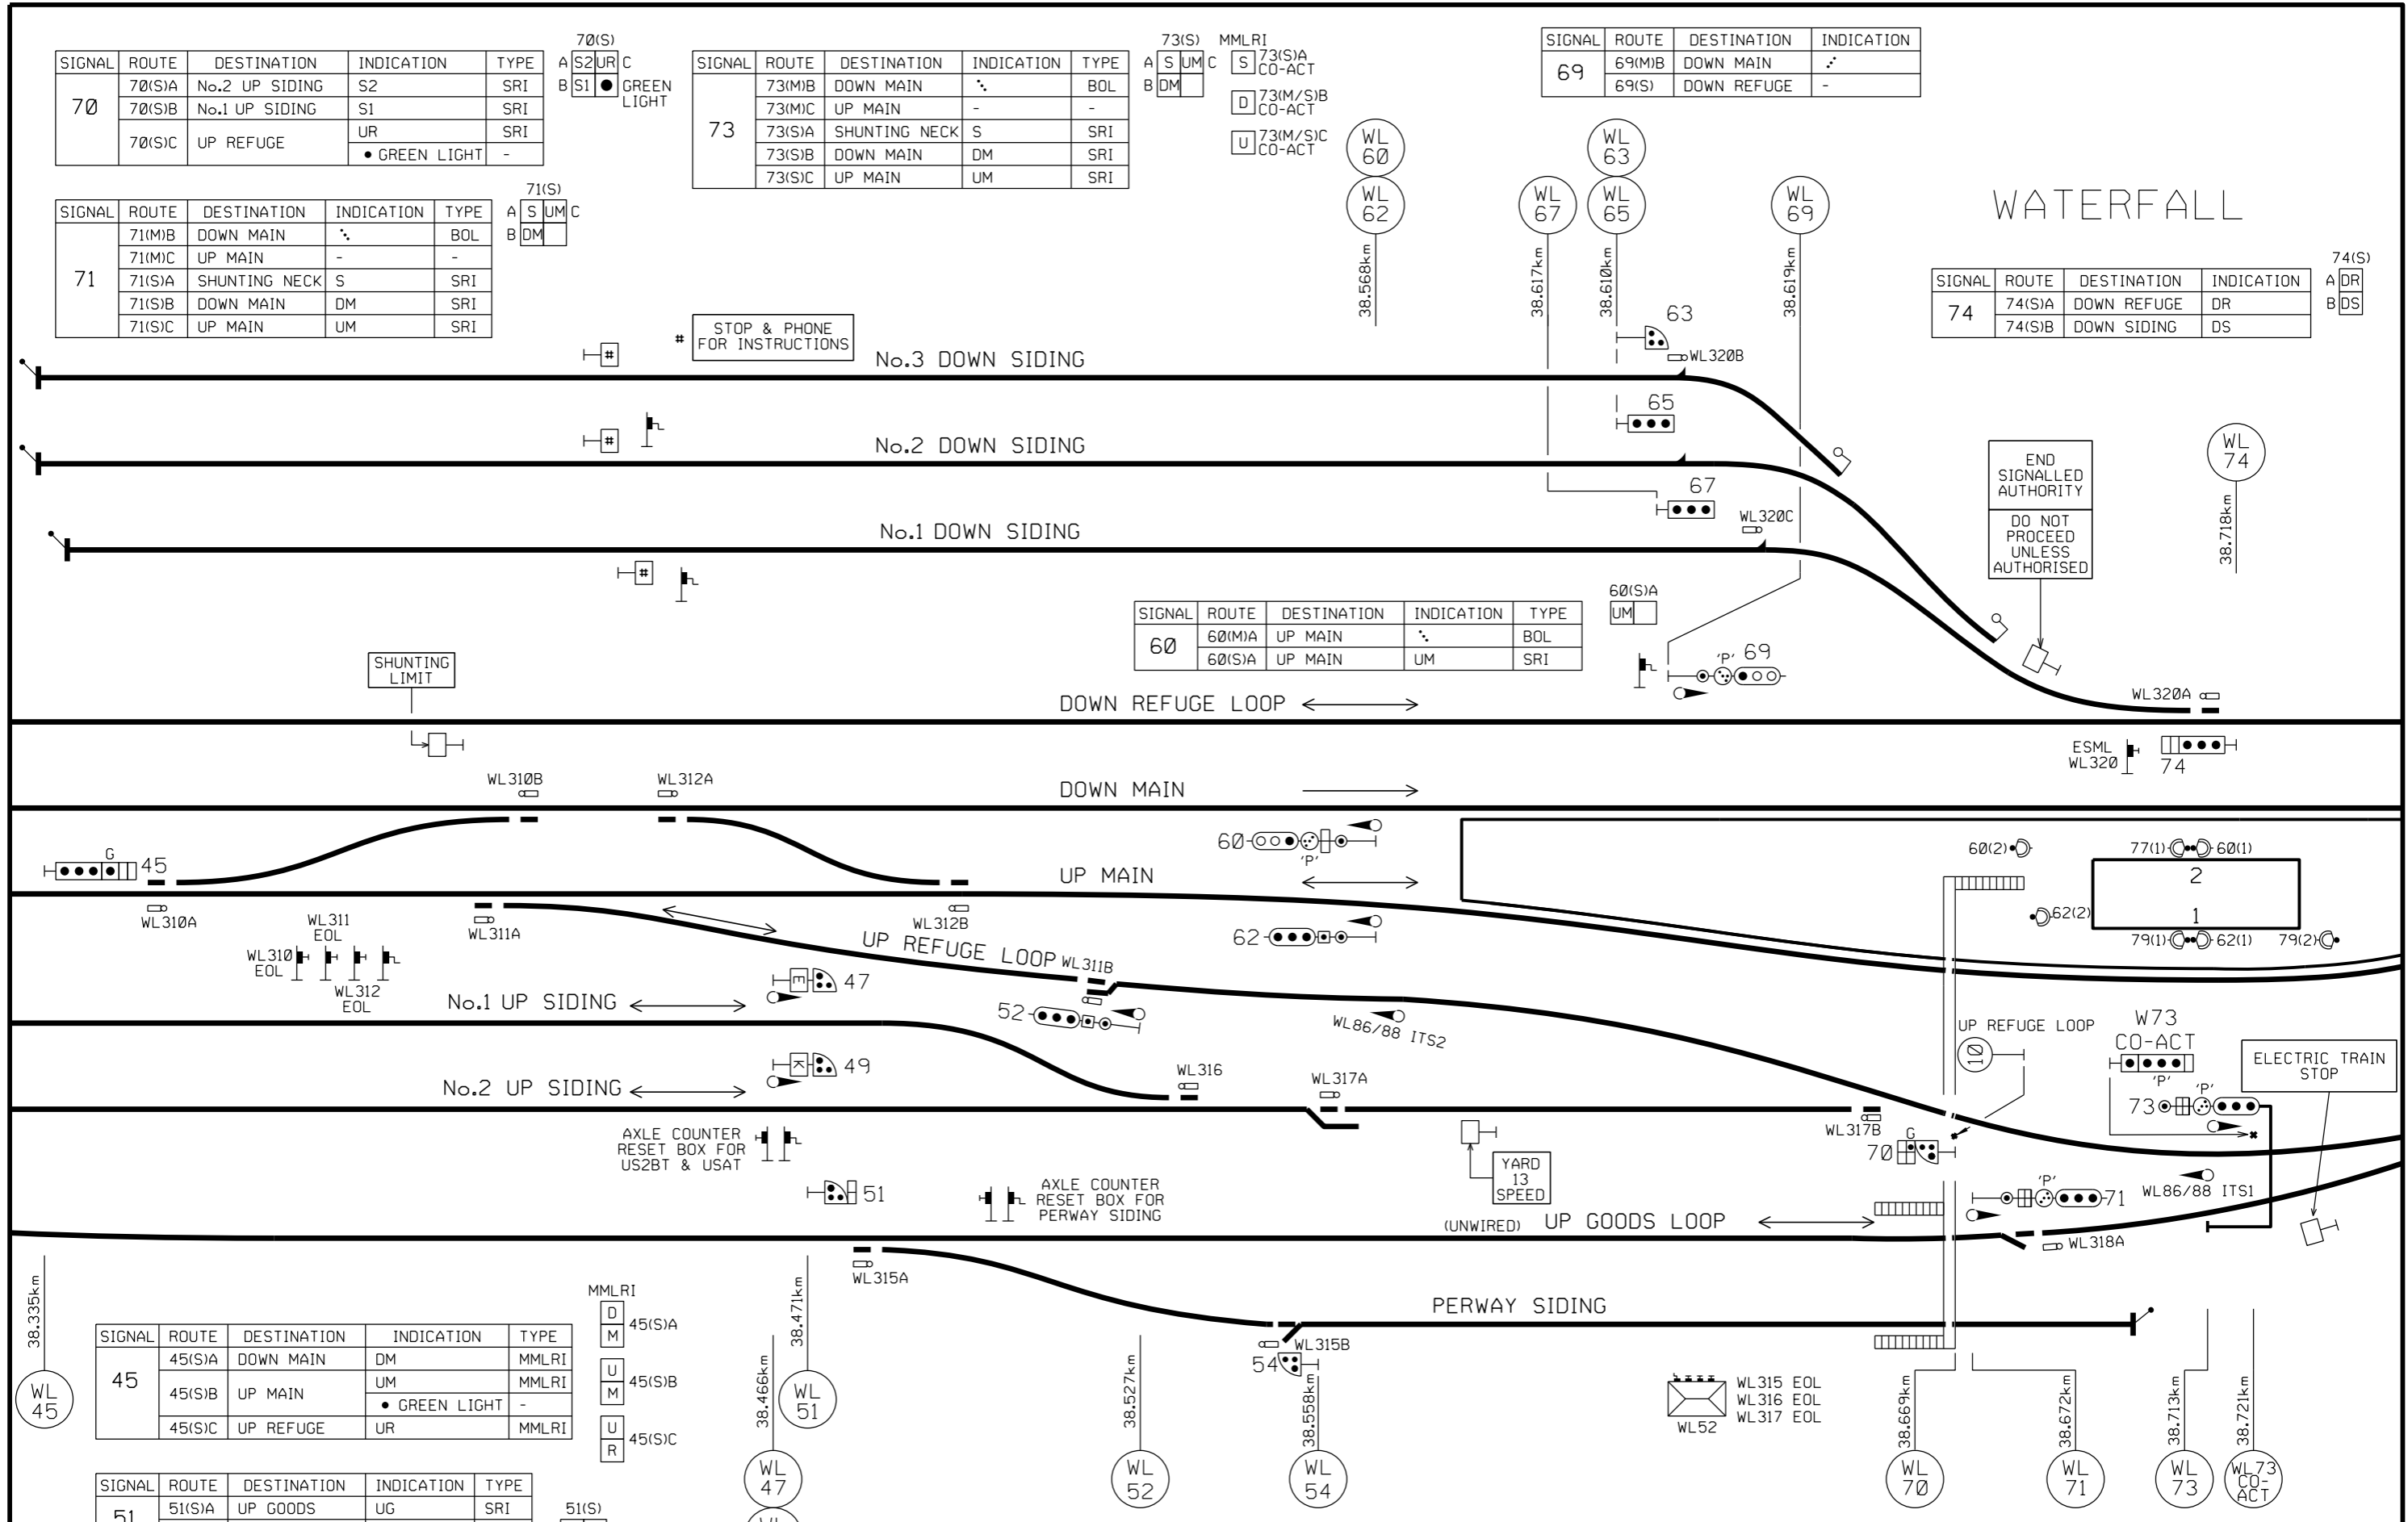

Transport for NSW

WATERFALL

MTMS2 WATERFALL STABLING FACILITY JULY 2024
DRIVERS DIAGRAM SHEET 3 OF 4

Produced by JMDR

VER. 06032024

SIGNAL	ROUTE	DESTINATION	INDICATION
83	83(S)A	SHUNTING NECK	S
	83(S)B	DOWN MAIN	DM

SIGNAL	ROUTE	DESTINATION	INDICATION
77	77(M)B	DOWN MAIN	-
	77(S)A	SHUNTING NECK	S
	77(S)B	DOWN MAIN	DM


SIGNAL	ROUTE	DESTINATION	INDICATION
84	84(S)A	UP REFUGE	UR
	84(S)B	UP MAIN	UM
	84(S)C	DOWN MAIN	DM
	84(S)D	DOWN REFUGE	DR

SIGNAL	ROUTE	DESTINATION	INDICATION
86	86(M)A	UP GOODS LOOP	⋅ + G
	86(M)B LSp	UP REFUGE	UR
	86(M)B BOL	UP REFUGE	⋅ + R
	86(M)C	UP MAIN	⋅ + U
	86(M)D	DOWN MAIN	-
	86(S)B	UP REFUGE	UR
	86(S)C	UP MAIN	UM
	86(S)E	DOWN REFUGE	DR

SIGNAL	ROUTE	DESTINATION	INDICATION
79	79(M)B	DOWN MAIN	⋅
	79(M)C	UP MAIN	-
	79(S)A	SHUNTING NECK	S
	79(S)B	DOWN MAIN	DM
	79(S)C	UP MAIN	UM

SIGNAL	ROUTE	DESTINATION	INDICATION
76	76(S)A	UP GOODS	UG
	76(S)B	UP REFUGE	UR • GREEN LIGHT

SIGNAL	ROUTE	DESTINATION	INDICATION
88	88(M)A	UP GOODS	⋅ + G
	88(M)B LSp	UP REFUGE	UR
	88(M)B BOL	UP REFUGE	⋅ + R
	88(S)B	UP REFUGE	UR
	88(S)C	UP MAIN	UM

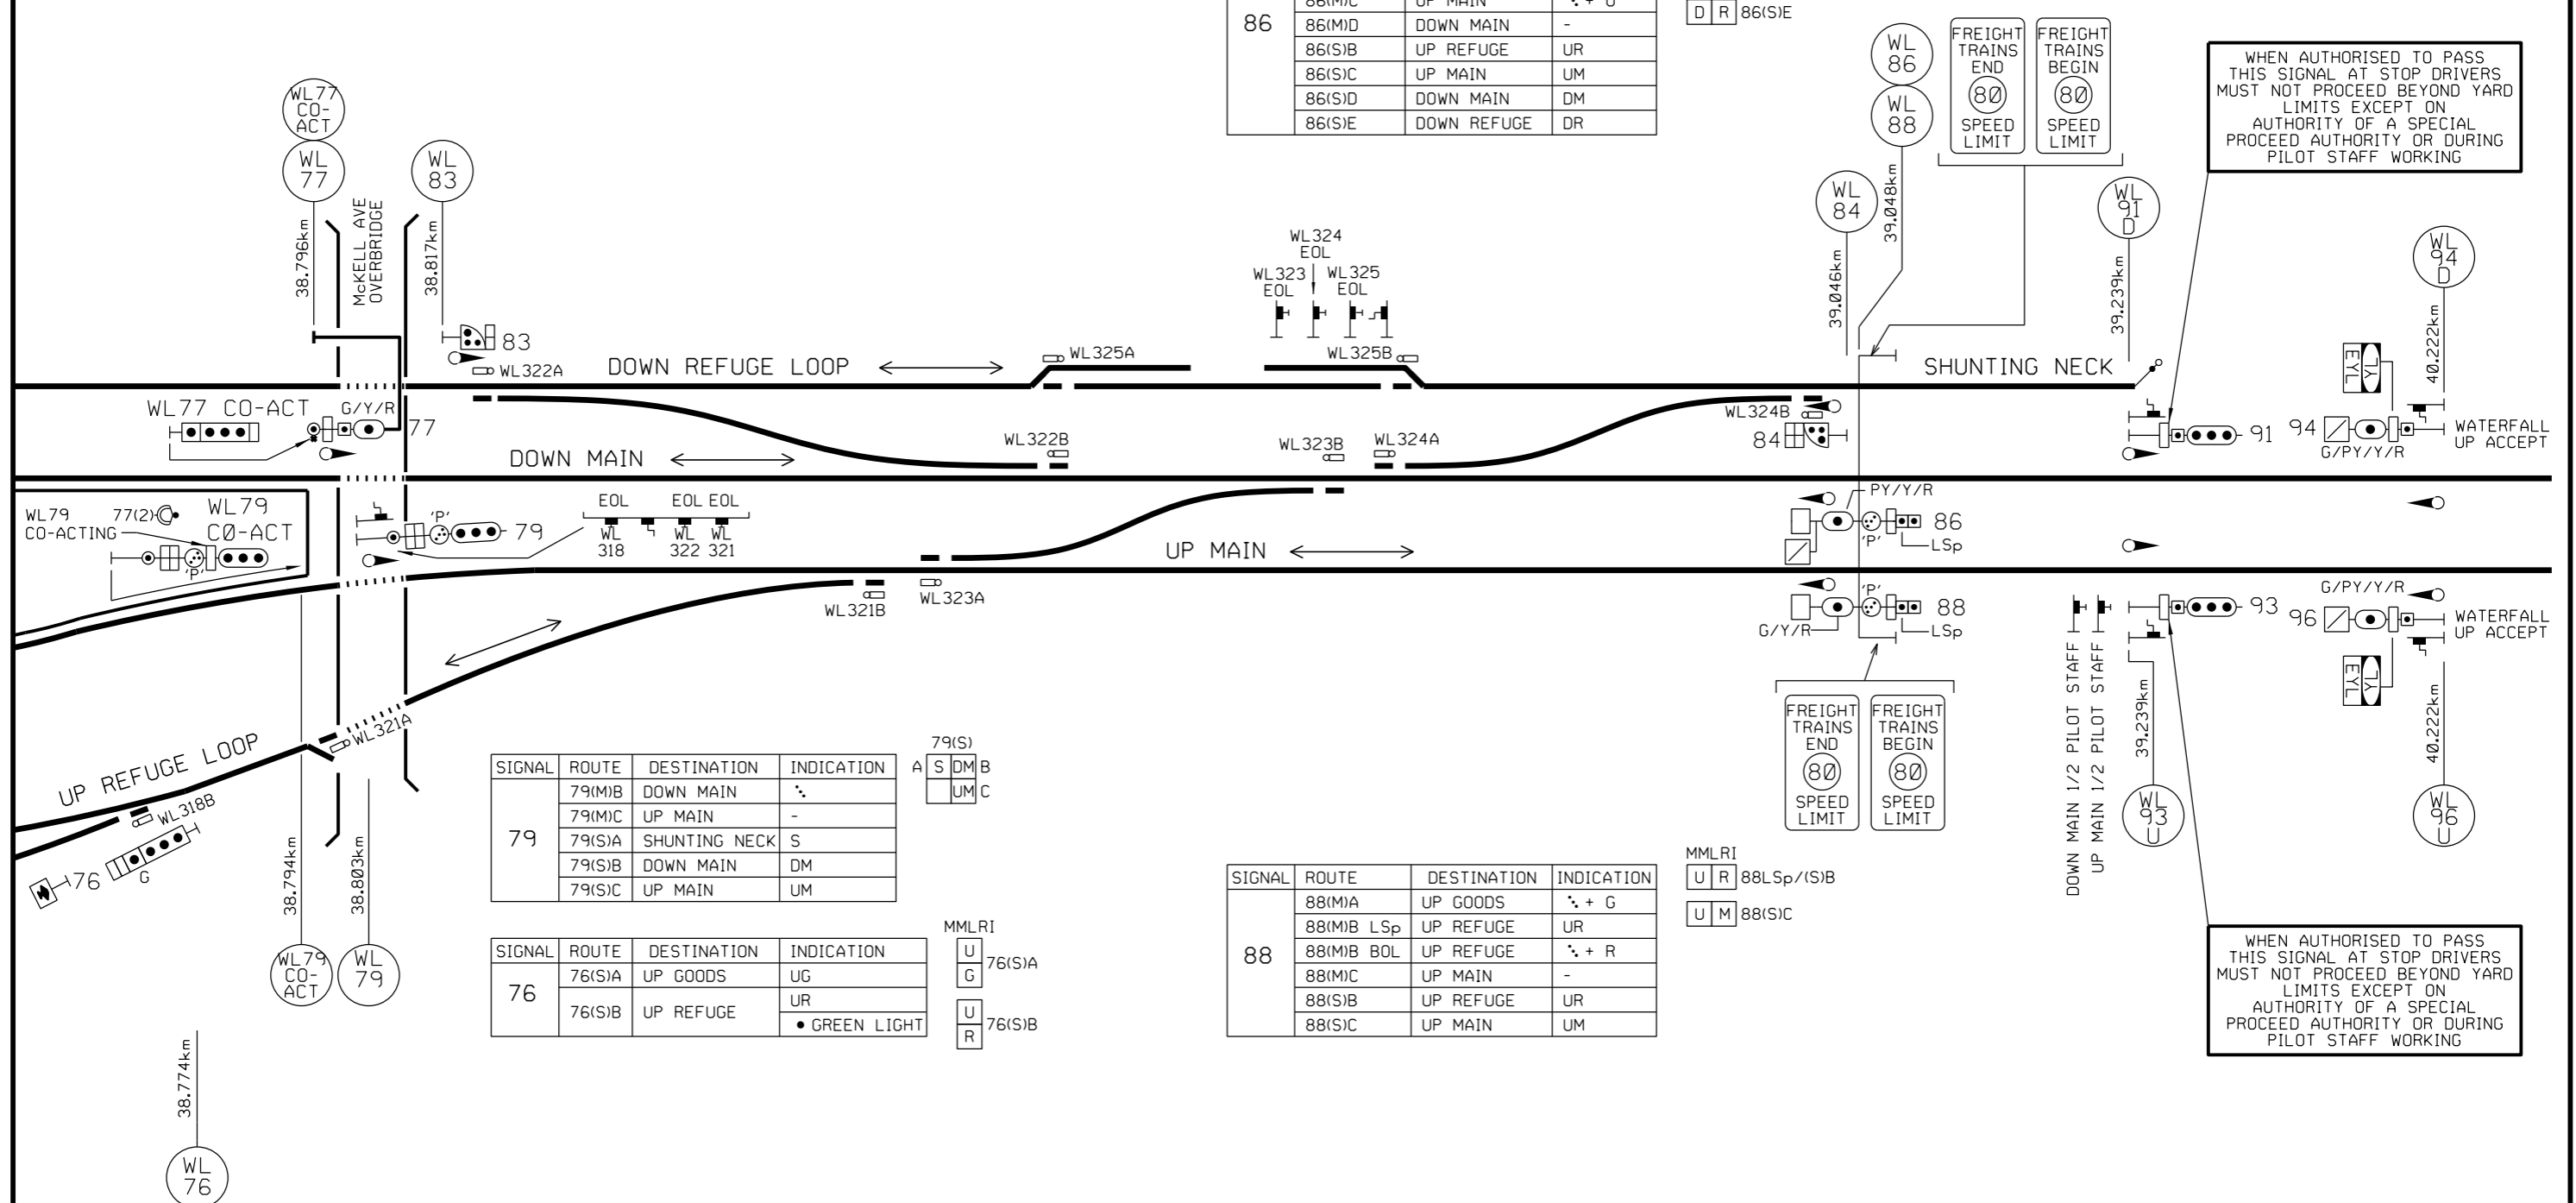

WHEN AUTHORISED TO PASS THIS SIGNAL AT STOP DRIVERS MUST NOT PROCEED BEYOND YARD LIMITS EXCEPT ON AUTHORITY OF A SPECIAL PROCEED AUTHORITY OR DURING PILOT STAFF WORKING

WHEN AUTHORISED TO PASS THIS SIGNAL AT STOP DRIVERS MUST NOT PROCEED BEYOND YARD LIMITS EXCEPT ON AUTHORITY OF A SPECIAL PROCEED AUTHORITY OR DURING PILOT STAFF WORKING



Transport for NSW

WATERFALL
MTMS2 WATERFALL STABLING FACILITY JULY 2024
DRIVERS DIAGRAM SHEET 4 OF 4

Produced by JMDR

VER. 06032024

OFFICIAL

BANKSTOWN – INSTALLATION OF NEW SIGNAL ARRANGEMENTS (UNCOMMISSIONED / BAGGED)

Since 0200 hours on **Monday, 17 June 2024** the following work was be carried out:

- Installation of new SM339 Co-Acting Signal (18.799km) this signal was installed and bagged with white cross attached to indicate this signal is uncommissioned.
- Installation of new Platform 1 Buffer Stop Light (18.699km) this light on post was installed and bagged with white cross attached to indicate this indication is uncommissioned.
- Installation of new P1 ITS Train Stop (18.740km) the Train Stop arm is strapped down and uncommissioned.
- Installation of new P2 ITS Train Stop (18.740km) the Train Stop arm is strapped down and uncommissioned.
- Installation of new SM341 Train Stop (18.803km) the Train Stop arm is strapped down and uncommissioned.
- Installation of new Advisory Board on Down Bankstown at (18 803km) this board was bagged to indicate this indication is uncommissioned.
- Installation of new Advisory Board on Up Bankstown at (18 799km) this board was bagged to indicate this indication is uncommissioned.

Mark Skribins

Signalling Commissioning Engineer

Tel: 0412 520 806

Email: Mark.Skribins@JMDR.comm

CONISTON (ILLAWARRA) - UPGRADE 120 SIGNAL TO LED TYPE

Commencing at **0200 hours on Saturday, 06 July 2024**, and continuing until 0200 hours on Monday, 08 July 2024, the following work will be carried out:

- Signal 120 on the Up North Fork Line will be upgraded to LED type at the same location. The Form of the Signal will remain the same.

VER27032024**Patricia Roser**

Commissioning Manager, Signalling
Engineering & Maintenance, Major Works, Sydney Trains
Mob: 0438461351
Email: patricia.rosier@transport.nsw.gov.au

Ken Hoang

Signal Design Engineer
Signalling & Control Systems, Engineering & System Integrity,
Sydney Trains
Mob: 0491215387
Email: ken.hoang@transport.nsw.gov.au

STATUS OF TOM NOTICES

<i>Number</i>	<i>Title</i>	<i>Issued</i>	<i>Effective</i>
018 – 2007	Emergency equipment boxes Rail	01/11/07	19/11/07
010 – 2012	48 Class: Train Operations Manual (TOM)	25/10/12	04/11/12
003 – 2013	48 Class: Wheels	07/02/13	10/02/13
015 – 2013	OMET 200: Minimum Standards for Electric Trains	30/05/13	09/06/13
002 – 2014	OMET 220: Wheelslip light indications	20/02/14	02/03/14
004 – 2016	OMET 262: Failure of Train Management System	14/07/16	24/07/16
004 – 2017	TWP 174 Ice Radio	20/07/17	31/07/17
018 - 2017	Amendment to OMET 200	14/12/17	24/12/17
012 – 2018	OMET 228 Control Circuit Failure	23/08/18	02/09/18
005 – 2018	OMET 242 Reverser handle jams in forward or reverse	18/08/18	28/08/18
006 – 2018	OMET 250 Applying power from the rear	18/08/18	28/08/18
008 – 2018	TWP 154 Responding to incapacitated Driver/Guard	18/08/18	28/08/18
016 - 2018	Network Rules Operational standards update	17/08/18	27/08/18
003 - 2019	OMET 264: Minimum Tractive Effort Requirements	21/02/19	03/03/19
012 – 2019	TWP 192: Working Trains Out of service	21/02/19	03/03/19
007 – 2019	TWP 136 Defective wheels	06/03/19	24/03/19
008 – 2019	TWP 190 Automatic Train Protection	06/03/19	24/03/19
009 – 2019	Train crew relieved in service & relay driver	06/03/19	24/03/19
004 – 2019	TWP 118 Reporting Faults	11/04/19	28/04/19
004 - 2020	TWP 124 Defective Brakes	20/05/20	08/06/20
005 - 2020	TWP 126 Defective Automatic Brakes	20/05/20	08/06/20
012 - 2020	WAR 202 Bogie Faults	20/05/20	08/06/20
011 - 2020	TWP 162 Train Crew Bell Signals	02/06/20	15/06/20
014 - 2020	TWP 112 Changing ends	20/07/20	03/08/20
017 - 2020	Operating Tangara, OSCAR, Millenium and Waratah with deflated air springs in the city underground	07/12/20	14/12/20
011 - 2021	Exception to OMET 200 & 350	17/11/21	29/11/21
005 - 2022	TWP 160 Driver procedure at stations	21/04/22	08/05/22
023 - 2022	Exception to OMET 254 Topside Preparation Locations	16/08/22	22/08/22
028 - 2022	Testing of Tangara Sets fitted with European Train Control System (ETCS) Level 1 & Level 2 (In cab signalling) equipment at Mortdale Maintenance Centre	08/12/22	16/12/22
027 - 2022	TWP 150: Damaged or Missing Window Glass	27/09/22	10/10/22
014 - 2023	Use of Automatic Train Protection (ATP) equipment on Millennium trains	20/02/23	05/03/23
016 - 2023	TWP 152 Disabled trains	07/03/23	20/03/23
017 - 2023	TWP 138 Assisting Trains using Emergency Couplers	07/03/23	20/03/23
022 – 2023	WB Radios on Waratah, Oscar, Millenium, Tangara and K sets	05/04/23	23/04/23
023 - 2023	OSCAR trains fitted with Automatic Train Protection (ATP) equipment	19/06/23	26/06/23
028 – 2023	TWP 176: Wayside Train Condition Monitoring	07/08/23	21/08/23

<i>Number</i>	<i>Title</i>	<i>Issued</i>	<i>Effective</i>
029 - 2023	Testing of an OSCAR Set (H5) with ETCS Level 2 equipment	01/09/23	04/09/23
026 – 2023	TWP 156: Operating doors	15/09/23	25/09/23
032 - 2023	TWP 100 Responsibilities of Train Crews	19/09/23	30/09/23
031 - 2023	Operation of Tangara trains fitted with ATP with Automatic Train Protection (ATP)	10/10/23	16/10/23
033 - 2023	Waratah (A and B SET) trains fitted with Automatic Train Protect equipment	17/10/23	23/10/23
034 - 2023	Testing Tangara trains fitted with ETCS Level 2	02/11/23	03/11/23
001 – 2024	TWP 182 Digital Train Radio	12/02/24	26/02/24
002 – 2024	Testing of a Millennium set (M31) with ETCS level 2 equipment	22/04/24	23/04/24
003 – 2024	Transition of NSW TrainLink Intercity Drivers and Guards to Sydney Trains	12/06/24	01/07/24

STATUS OF PERMANENT SAFE NOTICES

<i>Number</i>	<i>Title</i>	<i>Issued</i>	<i>Effective</i>
003 - 2024	Use of Signal Key Switches	11/04/24	26/04/24
001 - 2024	New Trackside Signage associated with Digital Systems Train Testing	08/02/24	24/02/24
002 - 2024	Compiling NRF 008 – Pilot Staff Notice	29/02/24	29/02/24
004 – 2024	Transition of NSW TrainLink Operations to Sydney Trains	12/06/24	01/07/24

Steve Swanson

Network Rules Specialist

Tel: 02 8922 4183 (external) 2 4183 (internal)

Email: stephen.swanson@transport.nsw.gov.au

STATUS OF NETWORK MANUALS AND FORMS**Network Manuals**

Network Local Appendices	RailSafe Website	Online documents
Operator Specific Procedures	RailSafe Website	Online documents
Network Rules	RailSafe Website	Online documents
Network Procedures	RailSafe Website	Online documents
Forms	RailSafe Website	Online documents (or order as applicable)

<i>Title</i>	<i>Status Sheet</i>	<i>Date issued</i>
<i>Train Working Procedures</i>		
TWP 100	TN 006 - 2021	April 2021
TWP 102	3	May 2012
TWP 108	4	May 2012
TWP 110	TN 009 - 2019	March 2019
TWP 112	TN 014 - 2020	August 2020
TWP 114	4	November 2015
TWP 116	3	May 2012
TWP 118	TN 004 - 2019	April 2019
TWP 120	3	May 2012
TWP 122	3	May 2012
TWP 124	TN 004 - 2020	May 2019
TWP 126	TN 005 - 2020	May 2019
TWP 128	3	May 2012
TWP 130	3	May 2012
TWP 132	3	May 2012
TWP 134	3	May 2012
TWP 136	TN 007 - 2019	March 2019
TWP 138	TN 017 - 2023	March 2023
TWP 142	3	May 2012
TWP 144	5	May 2012
TWP 146	3	May 2012
TWP 148	3	May 2012
TWP 150	TN 005 - 2017	April 2017
TWP 152	TN 016 - 2023	March 2023
TWP 154	TN 008 - 2018	July 2018
TWP 156	TN 011 - 2019	March 2019
TWP 158	3	May 2012
TWP 160	TN 005 - 2022	May 2022
TWP 162	TN 011- 2020	May 2019
TWP 164	4	May 2012
TWP 166	3	May 2012
TWP 168	3	May 2012
TWP 170	3	May 2012
TWP 172	4	May 2012
TWP 174	TN 004 - 2017	July 2017
TWP 176	TN 008 - 2017	July 2017
TWP 182	1	November 2015
TWP 188	1	November 2015
TWP 190	TN 008 - 2019	March 2019
TWP 192	TN 012 - 2019	March 2019

DISTRIBUTION OFFICERS**Sydney Trains****Safety and Environment****Maria Economou**

Safety Support

☎ 2 4502

🖨 2 1840

✉ Maria.Economou@transport.nsw.gov.au

Train Crew Operations**Manager Day of Operations**

☎ 8577 7029



TCOManagerDayofOperations@transport.nsw.gov.au

Train Crewing**Tim Kelly**

Operating Standards Officer

☎ 0422088764

✉ timothy.kelly@transport.nsw.gov.au

Service Delivery Response**Megan Parker**

Service Delivery Response

☎ 0491226502

✉ megan.parker@transport.nsw.gov.au

Leigh Lawton

Service Delivery Response

☎ 0418237261

✉ leigh.lawton@transport.nsw.gov.au

Maintenance**Fleet Maintenance****Hoshedar Movdawalla**

Fleet Maintenance Sydney Trains

☎ 2 0532

🖨 2 1274

✉ HOSHEDAR.MOVDAWALLA@transport.nsw.gov.au

Ram Ramaswamy

Fleet Maintenance Sydney Trains

☎ 2 0523

🖨 2 1274

✉ RAMYAVARAN.RAMASWAMY@transport.nsw.gov.au

Network Maintenance**Zaneta Janevski**

Engineering & Maintenance

☎ 87570199

✉ zaneta.janevski@transport.nsw.gov.au

Shannon Newton

Track Access Coordinator – North

☎ 95363791

✉ Shannon.Newton@transport.nsw.gov.au

Bradley Stewart

Territory Planning Manager - Central Coast/Hamilton

☎ 0476 833 911

✉ bradley.stewart@transport.nsw.gov.au

Ennio Soster

SCE

Project Delivery Electrical

☎ 25236

🖨 25917

✉ ENNIO.SOSTER@transport.nsw.gov.au

Daljit Kaur

Infrastructure Maintenance — Facilities

☎ 2 5922

🖨 2 5950

✉ Daljit.Kaur@transport.nsw.gov.au

Adrian Aquilina

Team leader - Strathfield Mains


☎ 97526610

✉ adrian.aquilina@transport.nsw.gov.au


Christina Morgan

Administration Support

ICON


 9379 6051 Christina.Morgan@transport.nsw.gov.au**Lorinda Melvin**

Administration Support


 0439510480 lorinda.melvin@transport.nsw.gov.au**Edward Lusik**

Team Leader Signals


CBD

 95368135 edward.lusik@transport.nsw.gov.au**Major Works****Greg Page**


Infrastructure Track

 25375 gregory.page@transport.nsw.gov.au**Michael Warner**


Signals and Electricity

 9848 9333 michael.warner@transport.nsw.gov.au**Logistics & Supply Chain****Murari Singh**



Contract Assurance Administrator

 02 9848 9698 Murari.Singh@transport.nsw.gov.au**Engineering & System Integrity****Yass Zahab**



Geotechnical Services

 2 7589  2 7786 Yassine.El-Zahab@transport.nsw.gov.au**Richard Agostino**



C and CS

 2 0875 9 2137 Richard.Agostino@transport.nsw.gov.au**Human Resources****Robert Neloski**



Training — Learning and Development

 2 7567 robert.neloski@transport.nsw.gov.au**Peter Nilon**


Survey Group

 9848 9904 peter.nilon@transport.nsw.gov.au**Trainlink****Phillip Antonioli**



Operational Improvement Manager

 8574 2960 0417694249 Phillip.antonioli@transport.nsw.gov.au**Ashley Brandse**



Associate Director Operations North & Central

 4962 9820 ASHLEY.BRANDSE@transport.nsw.gov.au**Robert Blanch**

Area Manager Hunter & Regional North



 43499210 0458261501 ROBERT.BLANCH@transport.nsw.gov.au**Netti Byrnes**

Area Manager Central Coast


 43499210 0458261501 Annette.Byrnes@transport.nsw.gov.au

Leisa Case

Area Manager Central Intercity

  0429900371 Annette.Byrnes@transport.nsw.gov.au**Dwayne Purcell**



Area Manager Central Regional

 0428670580


DWAYNE.PURCELL@transport.nsw.gov.au

Michael Dorrian

Area Manager South Coast

  0439743316 Michael.dorrian@transport.nsw.gov.au**Ian Modon**

Area Manager South Main

 0427016255

NOTES

NOTES

NOTICE TO SUBSCRIBERS

The Weekly Notice is issued every Tuesday, and takes effect on the following Monday.

Those who require the Weekly Notice must ensure that they receive it and are aware of the changes that affect their work duties and responsibilities.

Director Network Standards, Systems & Quality**Sydney Trains**

Level 4, 36-46 George Street

Burwood NSW 2134

Tuesday, 11 June 2024
